


ISAC Target Hall Schedule-Feb 23 to Apr15

By David Wang

Updated 27-Feb-2015

ID	Task Mode	Task Name	Duration	Start	Finish	Feb 22, '15		Mar 1, '15			Mar 8, '15				Mar 15, '15			Mar 22, '15				Mar 29, '15			Apr 5, '15				Apr 12, '15			Apr 19, '15			
						S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M
1		Pre- Module Move	9 days	Mon 2/23/15	Thu 3/5/15	[Gantt bar for Pre- Module Move]																													
2		Pedal Wheels and Coils Replacement- ITE	1 day	Mon 2/23/15	Mon 2/23/15	[Gantt bar for Pedal Wheels and Coils Replacement- ITE]																													
3		Storage of 6 old Turbo Pumps to Cyclotron Vault	1 day	Tue 2/24/15	Tue 2/24/15	[Gantt bar for Storage of 6 old Turbo Pumps to Cyclotron Vault]																													
4		Pedal wheels and Coils Replacement-ITW	1 day	Wed 2/25/15	Wed 2/25/15	[Gantt bar for Pedal wheels and Coils Replacement-ITW]																													
5		Primary and Secondary Vacuum Vessel Leak Check-ITE	3 days	Mon 3/2/15	Wed 3/4/15	[Gantt bar for Primary and Secondary Vacuum Vessel Leak Check-ITE]																													
6		5 Shielding Block Move-Storage Area to ITE	1 day	Thu 3/5/15	Thu 3/5/15	[Gantt bar for 5 Shielding Block Move-Storage Area to ITE]																													
7		TM1 Move/Spent Target	3 days	Mon 3/9/15	Wed 3/11/15	[Gantt bar for TM1 Move/Spent Target]																													
8		Cameras Set up-ITW	0.25 days	Mon 3/9/15	Mon 3/9/15	[Gantt bar for Cameras Set up-ITW]																													
9		Module Move-TM1-ITW to SHC	0.25 days	Mon 3/9/15	Mon 3/9/15	[Gantt bar for Module Move-TM1-ITW to SHC]																													
10		Target Removal/Electrical Check-TM1-ThO-SHC	0.5 days	Mon 3/9/15	Mon 3/9/15	[Gantt bar for Target Removal/Electrical Check-TM1-ThO-SHC]																													
11		Module Move-TM1-SHC to Silo	1 day	Tue 3/10/15	Tue 3/10/15	[Gantt bar for Module Move-TM1-SHC to Silo]																													
12		Spent Target Move-ThO-SHC to Vault	1 day	Wed 3/11/15	Wed 3/11/15	[Gantt bar for Spent Target Move-ThO-SHC to Vault]																													
13		RPG test on TM1 ThO target	3 days	Mon 3/9/15	Wed 3/11/15	[Gantt bar for RPG test on TM1 ThO target]																													
14		TM4 Move/Spent Target	4 days	Thu 3/12/15	Tue 3/17/15	[Gantt bar for TM4 Move/Spent Target]																													
15		5 shielding block move out of ITE/Argon Venting ITE	0.5 days	Thu 3/12/15	Thu 3/12/15	[Gantt bar for 5 shielding block move out of ITE/Argon Venting ITE]																													
16		Cameras Set up-ITE	0.5 days	Thu 3/12/15	Thu 3/12/15	[Gantt bar for Cameras Set up-ITE]																													
17		Module Move-TM4-ITE to SHC	0.5 days	Fri 3/13/15	Fri 3/13/15	[Gantt bar for Module Move-TM4-ITE to SHC]																													
18		Target Removal/Electrical Check-TM4-UCx-SHC	0.5 days	Fri 3/13/15	Fri 3/13/15	[Gantt bar for Target Removal/Electrical Check-TM4-UCx-SHC]																													
19		Module Move-TM4 -SHC to Silo	1 day	Mon 3/16/15	Mon 3/16/15	[Gantt bar for Module Move-TM4 -SHC to Silo]																													
20		Spent Target Move-UCx-SHC to Vault	1 day	Tue 3/17/15	Tue 3/17/15	[Gantt bar for Spent Target Move-UCx-SHC to Vault]																													
21		Handrail Holes Coring	5 days	Wed 3/18/15	Tue 3/24/15	[Gantt bar for Handrail Holes Coring]																													
22		New Holes Coring-preparation	2 days	Wed 3/18/15	Thu 3/19/15	[Gantt bar for New Holes Coring-preparation]																													
23		New Holes Coring-Westcoast coring	2 days	Fri 3/20/15	Mon 3/23/15	[Gantt bar for New Holes Coring-Westcoast coring]																													
24		Clean up/Re-position	1 day	Tue 3/24/15	Tue 3/24/15	[Gantt bar for Clean up/Re-position]																													
25		Leak Check -ITW BV1,BV2, and Vacuum Lines	1 day	Wed 3/25/15	Wed 3/25/15	[Gantt bar for Leak Check -ITW BV1,BV2, and Vacuum Lines]																													
26		First HP Ta Surface Target on TM4 Ready for ITE	14 days	Thu 3/26/15	Tue 4/14/15	[Gantt bar for First HP Ta Surface Target on TM4 Ready for ITE]																													
27		HP Ta Surface Target Insert into SHC	0.25 days	Thu 3/26/15	Thu 3/26/15	[Gantt bar for HP Ta Surface Target Insert into SHC]																													
28		Module Move-TM4-Silo to SHC	0.75 days	Thu 3/26/15	Thu 3/26/15	[Gantt bar for Module Move-TM4-Silo to SHC]																													
29		Target Installation-TM4-HP Ta/Leak Check/Electrical Check	0.5 days	Fri 3/27/15	Fri 3/27/15	[Gantt bar for Target Installation-TM4-HP Ta/Leak Check/Electrical Check]																													
30		Module Move-TM4-SHC to CS	0.5 days	Fri 3/27/15	Fri 3/27/15	[Gantt bar for Module Move-TM4-SHC to CS]																													
31		Connection and Pump down -TM4 at CS	1 day	Mon 3/30/15	Mon 3/30/15	[Gantt bar for Connection and Pump down -TM4 at CS]																													
32		Pump Down/Helium pressure test- TM4 at CS	2 days	Tue 3/31/15	Wed 4/1/15	[Gantt bar for Pump Down/Helium pressure test- TM4 at CS]																													
33		Cameras set up-ITE/TM4 and CS venting	0.25 days	Thu 4/2/15	Thu 4/2/15	[Gantt bar for Cameras set up-ITE/TM4 and CS venting]																													
34		Module Move-TM4-CS to ITE	0.75 days	Thu 4/2/15	Thu 4/2/15	[Gantt bar for Module Move-TM4-CS to ITE]																													
35		connection and Pump down -TM4 at ITE	0.5 days	Fri 4/3/15	Fri 4/3/15	[Gantt bar for connection and Pump down -TM4 at ITE]																													
36		Pump down/ Conditioning- TM4 at ITE	6.5 days	Fri 4/3/15	Mon 4/13/15	[Gantt bar for Pump down/ Conditioning- TM4 at ITE]																													
37		5 Shielding Blocks Move-Storage Area to ITE/ ITE Ready	1 day	Tue 4/14/15	Tue 4/14/15	[Gantt bar for 5 Shielding Blocks Move-Storage Area to ITE/ ITE Ready]																													

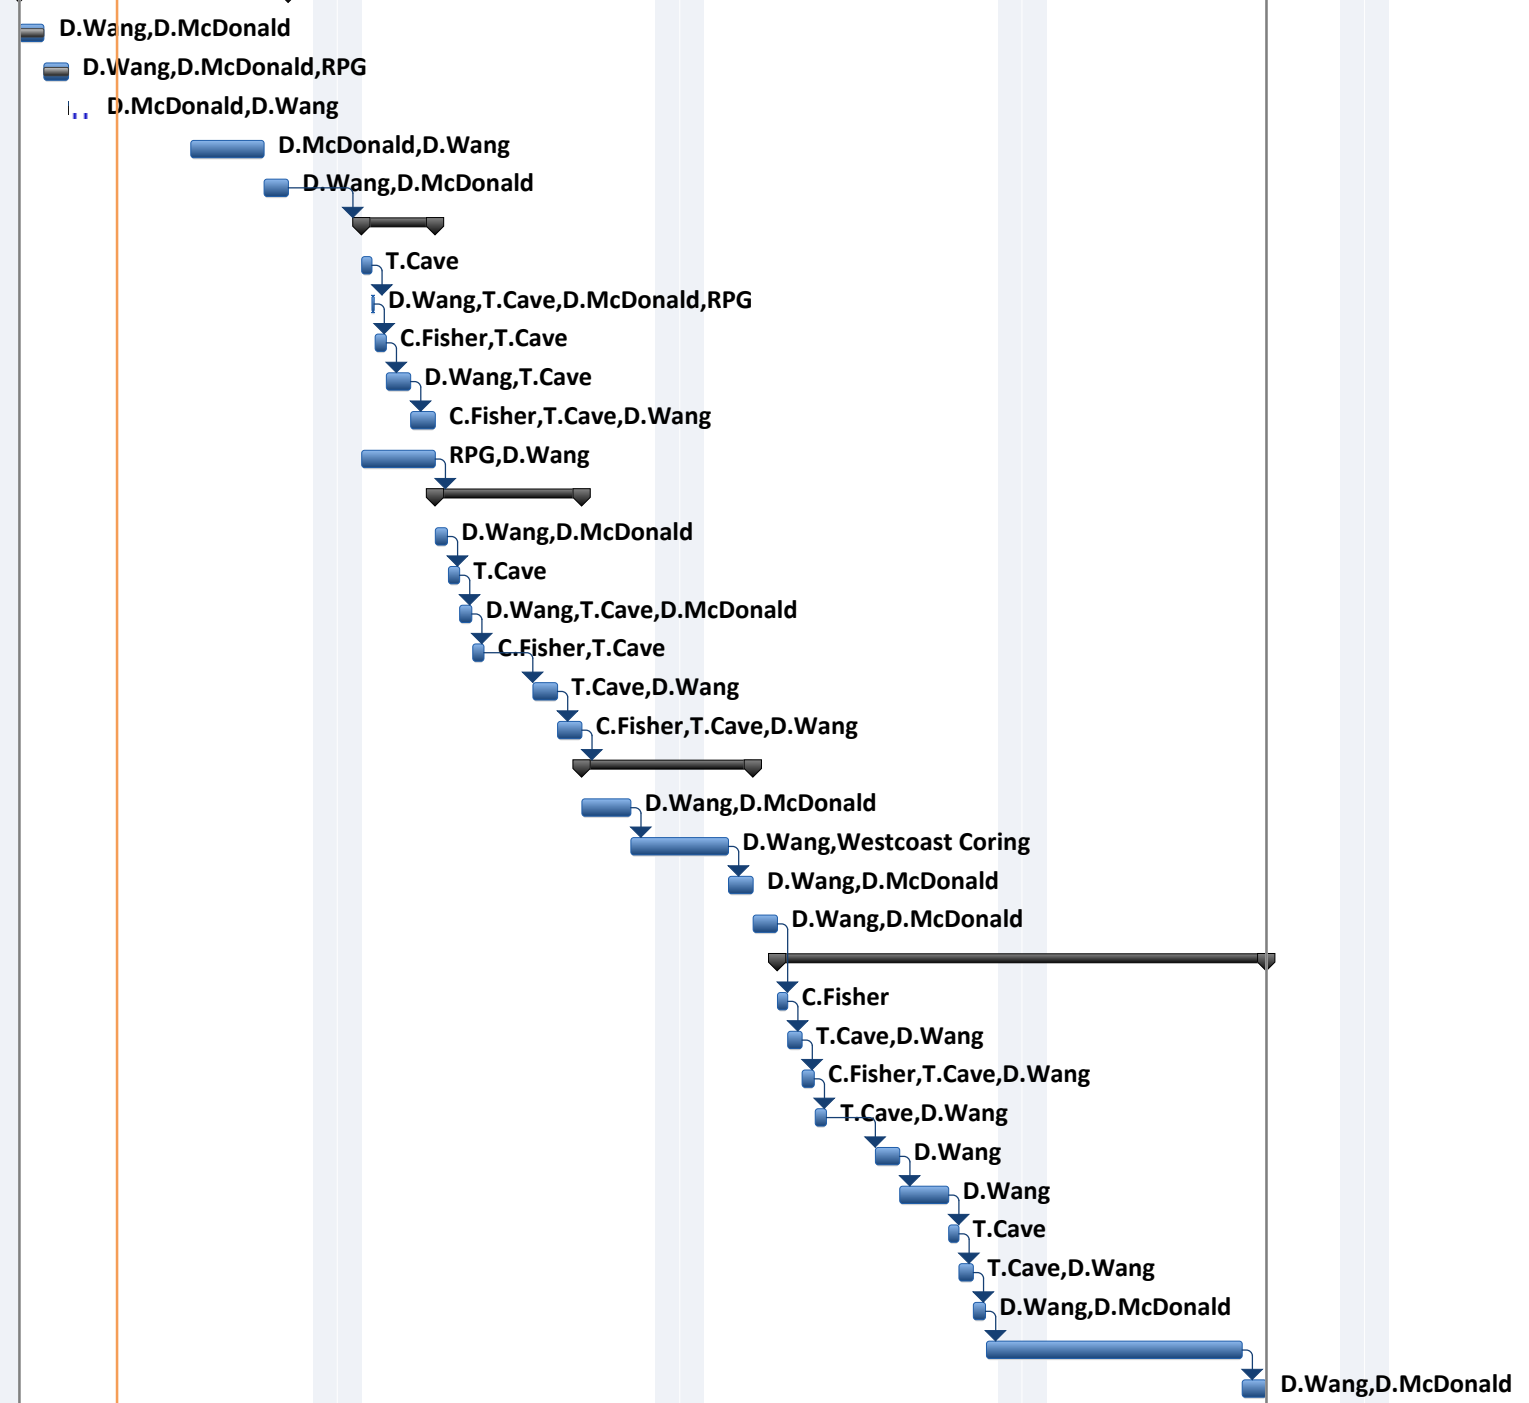

Project: Target Hall shut down act Date: Fri 2/27/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
