


ISAC Target Hall Schedule-Feb 23 to Apr15

By David Wang

Updated 27-Feb-2015

ID	Task Mode	Task Name	Duration	Start	Feb 22, '15				Mar 1, '15			Mar 8, '15				Mar 15, '15			Mar 22, '15				Mar 29, '15			Apr 5, '15				Apr 12, '15		
					S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	
1	✓	Pre- Module Move	9 days	Mon 2/23/15																												
2	✓	Pedal Wheels and Coils Replacement- ITE	1 day	Mon 2/23/15																												
3	✓	Storage of 6 old Turbo Pumps to Cyclotron Vault	1 day	Tue 2/24/15																												
4	✓	Pedal wheels and Coils Replacement-ITW	1 day	Wed 2/25/15																												
5	✓	Primary and Secondary Vacuum Vessel Leak Check-ITE	3 days	Mon 3/2/15																												
6	✓	5 Shielding Block Move-Storage Area to ITE	1 day	Thu 3/5/15																												
7	✓	TM1 Move/Spent Target	5 days	Mon 3/9/15																												
8	✓	Cameras Set up-ITW	0.25 days	Mon 3/9/15																												
9	✓	Module Move-TM1-ITW to SHC	0.25 days	Mon 3/9/15																												
10	✓	Target Removal/Electrical Check-TM1-ThO-SHC	0.5 days	Mon 3/9/15																												
11	✓	Module Move-TM1-SHC to Silo	0.5 days	Tue 3/10/15																												
12	✓	RPG Test on TM1 ThO Target	1.5 days	Tue 3/10/15																												
13	✓	ThO Target Autopsy/Shielding Blocks Move-ITE to ITW/Cameras Set up -ITE	1 day	Thu 3/12/15																												
14	✓	Spent Target Move-ThO-SHC to Vault/Argon Vent ITE	0.5 days	Fri 3/13/15																												
15	✓	Module Move-TM2-CS to Silo	0.5 days	Fri 3/13/15																												
16	✓	TM4 Move/Spent Target	3 days	Mon 3/16/15																												
17	✓	Module Move-TM4-ITE to SHC	0.5 days	Mon 3/16/15																												
18	✓	Target Removal/Electrical Check-TM4-UCx-SHC	0.5 days	Mon 3/16/15																												
19	✓	Module Move-TM4 -SHC to CS	1 day	Tue 3/17/15																												

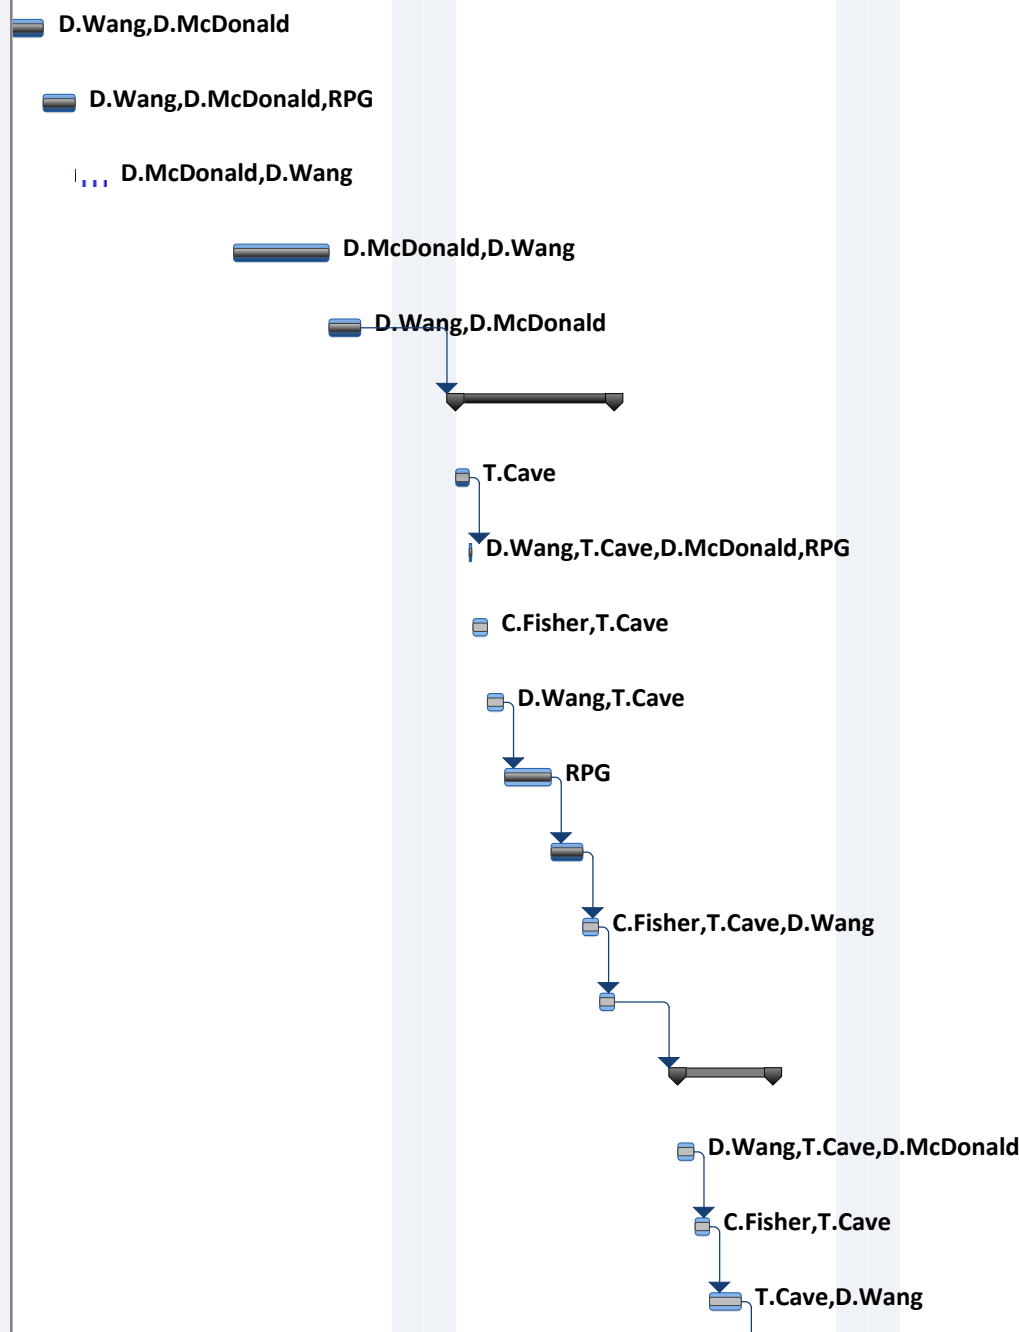

Project: Target Hall shut down act Date: Thu 4/2/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

