

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 5, '15				Apr 12, '15			Apr 19, '15				Apr 26, '15			May 3
								S	M	W	F	S	T	T	S	M	W	F	S	T	T	S
1		TM4 Ta#45 ready for Bear	4 days	Tue 4/7/15	Fri 4/10/15																	
2		Grounding Test-ITW, ITE	1 day	Tue 4/7/15	Tue 4/7/15																	
3		Foot Anchors Grout-ITW	2.5 days	Wed 4/8/15	Fri 4/10/15	2																
4		Shielding Blocks Move-I'	0.5 days	Fri 4/10/15	Fri 4/10/15	3																
5		TM1-TM2-TM4 Target Hal	55 days	Mon 4/13/15	Fri 6/26/15																	
6		TM1 UCx Ready for Be	8 days	Fri 4/17/15	Tue 4/28/15																	
7		New Ucx Target in SH	0.2 days	Fri 4/17/15	Fri 4/17/15		A.Mjos,I.Earle,T.Cave															
8		Moduel Move-TM1-S	0.2 days	Fri 4/17/15	Fri 4/17/15	7	T.Cave,D.Wang															
9		Ucx target install /Lea	0.2 days	Fri 4/17/15	Fri 4/17/15	8	I.Earle,T.Cave,D.W															
10		Module Move- TM1 -	0.2 days	Fri 4/17/15	Fri 4/17/15	9	D.Wang,T.Cave															
11		TM1 Vacuum Connec	0.2 days	Fri 4/17/15	Fri 4/17/15	10	D.Wang															
12		Heium Pressure Test-	0.5 days	Mon 4/20/15	Mon 4/20/15	11	D.Wang															
13		TM1 Connect at CS/I	0.5 days	Mon 4/20/15	Mon 4/20/15	12	D.Wang,D.McDona															
14		Module Conditioning	4.5 days	Tue 4/21/15	Mon 4/27/15	13	A.Mjos															
15		Finish of Conditioning	0.5 days	Mon 4/27/15	Mon 4/27/15	14	D.Wang															
16		Argon Vent CS /ITW c	0.25 days	Tue 4/28/15	Tue 4/28/15	15	D.Wang,T.Cave															
17		Module Move -TM1-(0.25 days	Tue 4/28/15	Tue 4/28/15	16	D.Wang,T.Cave															
18		Module Connect-TM1	0.5 days	Tue 4/28/15	Tue 4/28/15	17	D.Wang,D.McDona															
19		TM2 Refurbishment Co	55 days	Mon 4/13/15	Fri 6/26/15																	
20		TM2 Top Service Cap	3 days	Mon 4/13/15	Wed 4/15/15		D.Wang															
21		Module Move -TM2-S	1 day	Thu 4/30/15	Thu 4/30/15		T.Cave,D.Wang															
22		TM2 Wiring Prepare/	1 day	Fri 5/1/15	Fri 5/1/15	21	D.Wang,T.Cave															
23		TM2 Wiring - SHC & T	2 days	Mon 5/4/15	Tue 5/5/15	22	T.Cave,C.Fisher,D.V															
24		Module Move-TM2-S	1 day	Wed 5/6/15	Wed 5/6/15	23	T.Cave,D.Wang															
25		Source Tray Install on	1 day	Thu 5/7/15	Thu 5/7/15	24	D.Wang,C.Fisher,T.															
26		TM2 Wiring- CS & Ser	2 days	Fri 5/8/15	Mon 5/11/15	25,20	T.Cave,D.Jackson,D															
27		Remove Transfer tabl	1 day	Tue 5/12/15	Tue 5/12/15	25	C.Fisher,T.Cave,D.V															
28		TM2 Wiring-CS & Ser	1 day	Wed 5/13/15	Wed 5/13/15	27	T.Cave,D.Jackson,D															
29		Module Move- TM2 -	1 day	Thu 5/14/15	Thu 5/14/15	28	T.Cave,D.Wang															
30		Leak, Electrical Check	1 day	Mon 5/25/15	Mon 5/25/15	29	C.Fisher,T.Cave,D.V															
31		Module Move-TM2-S	1 day	Tue 5/26/15	Tue 5/26/15	30	T.Cave,D.Wang															
32		Helium Pressure Test	2 days	Wed 5/27/15	Thu 5/28/15	31	D.Wang															
33		Module Move -TM2-(1 day	Fri 5/29/15	Fri 5/29/15	32	D.Wang,T.Cave															
34		TM2 Dummy Target I	0.5 days	Thu 6/11/15	Thu 6/11/15	33,51	C.Fisher,A.Mjos															
35		Module Move-TM2-S	0.5 days	Thu 6/11/15	Thu 6/11/15	34	T.Cave,D.Wang															
36		Dummy Target Install	0.5 days	Fri 6/12/15	Fri 6/12/15	35	C.Fisher,T.Cave,D.V															
37		Module Move- TM2 -	0.5 days	Fri 6/12/15	Fri 6/12/15	36	D.Wang,T.Cave															
38		Helium Pressure Test	1 day	Tue 6/16/15	Tue 6/16/15	37	D.Wang															
39		TM2 Test at CS	7 days	Wed 6/17/15	Thu 6/25/15	38	A.Mjos,G.Minor,D.															

Project: Target Hall Scheduled Act Date: Mon 4/20/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 5, '15				Apr 12, '15			Apr 19, '15			Apr 26, '15			May 3
								S	M	W	F	S	T	T	S	M	W	F	S	T	T
40		TM2 Fully Operational	1 day	Fri 6/26/15	Fri 6/26/15	39															
41		TM4 HpSiC Ready for B	21 days	Fri 5/22/15	Fri 6/19/15																
42		Shielding Blocks Move	1 day	Fri 5/22/15	Fri 5/22/15	18	D.Wang,D.McDona														
43		New HP SiC Target in	1 day	Mon 6/1/15	Mon 6/1/15	33	C.Fisher,A.Mjos														
44		Cameras set up/Mod	0.5 days	Tue 6/2/15	Tue 6/2/15	43	T.Cave,D.Wang														
45		New SiC Target Instal	0.5 days	Tue 6/2/15	Tue 6/2/15	44	C.Fisher,D.Wang,T.														
46		Module Move-TM4-S	1 day	Wed 6/3/15	Wed 6/3/15	45	D.Wang,T.Cave														
47		Helium Pressure Test	0.5 days	Thu 6/4/15	Thu 6/4/15	46	D.Wang														
48		Module Conditioning	3 days	Thu 6/4/15	Tue 6/9/15	47	A.Mjos														
49		Finish of Conditioning	0.5 days	Tue 6/9/15	Tue 6/9/15	48	D.Wang														
50		Module Move -TM4-	0.5 days	Wed 6/10/15	Wed 6/10/15	49	T.Cave,D.Wang														
51		Module Connect-TM	0.5 days	Wed 6/10/15	Wed 6/10/15	50	D.Wang,D.McDona														
52		Shielding Blocks Move	1 day	Fri 6/19/15	Fri 6/19/15	51	D.Wang,D.McDona														

Project: Target Hall Scheduled Act
Date: Mon 4/20/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

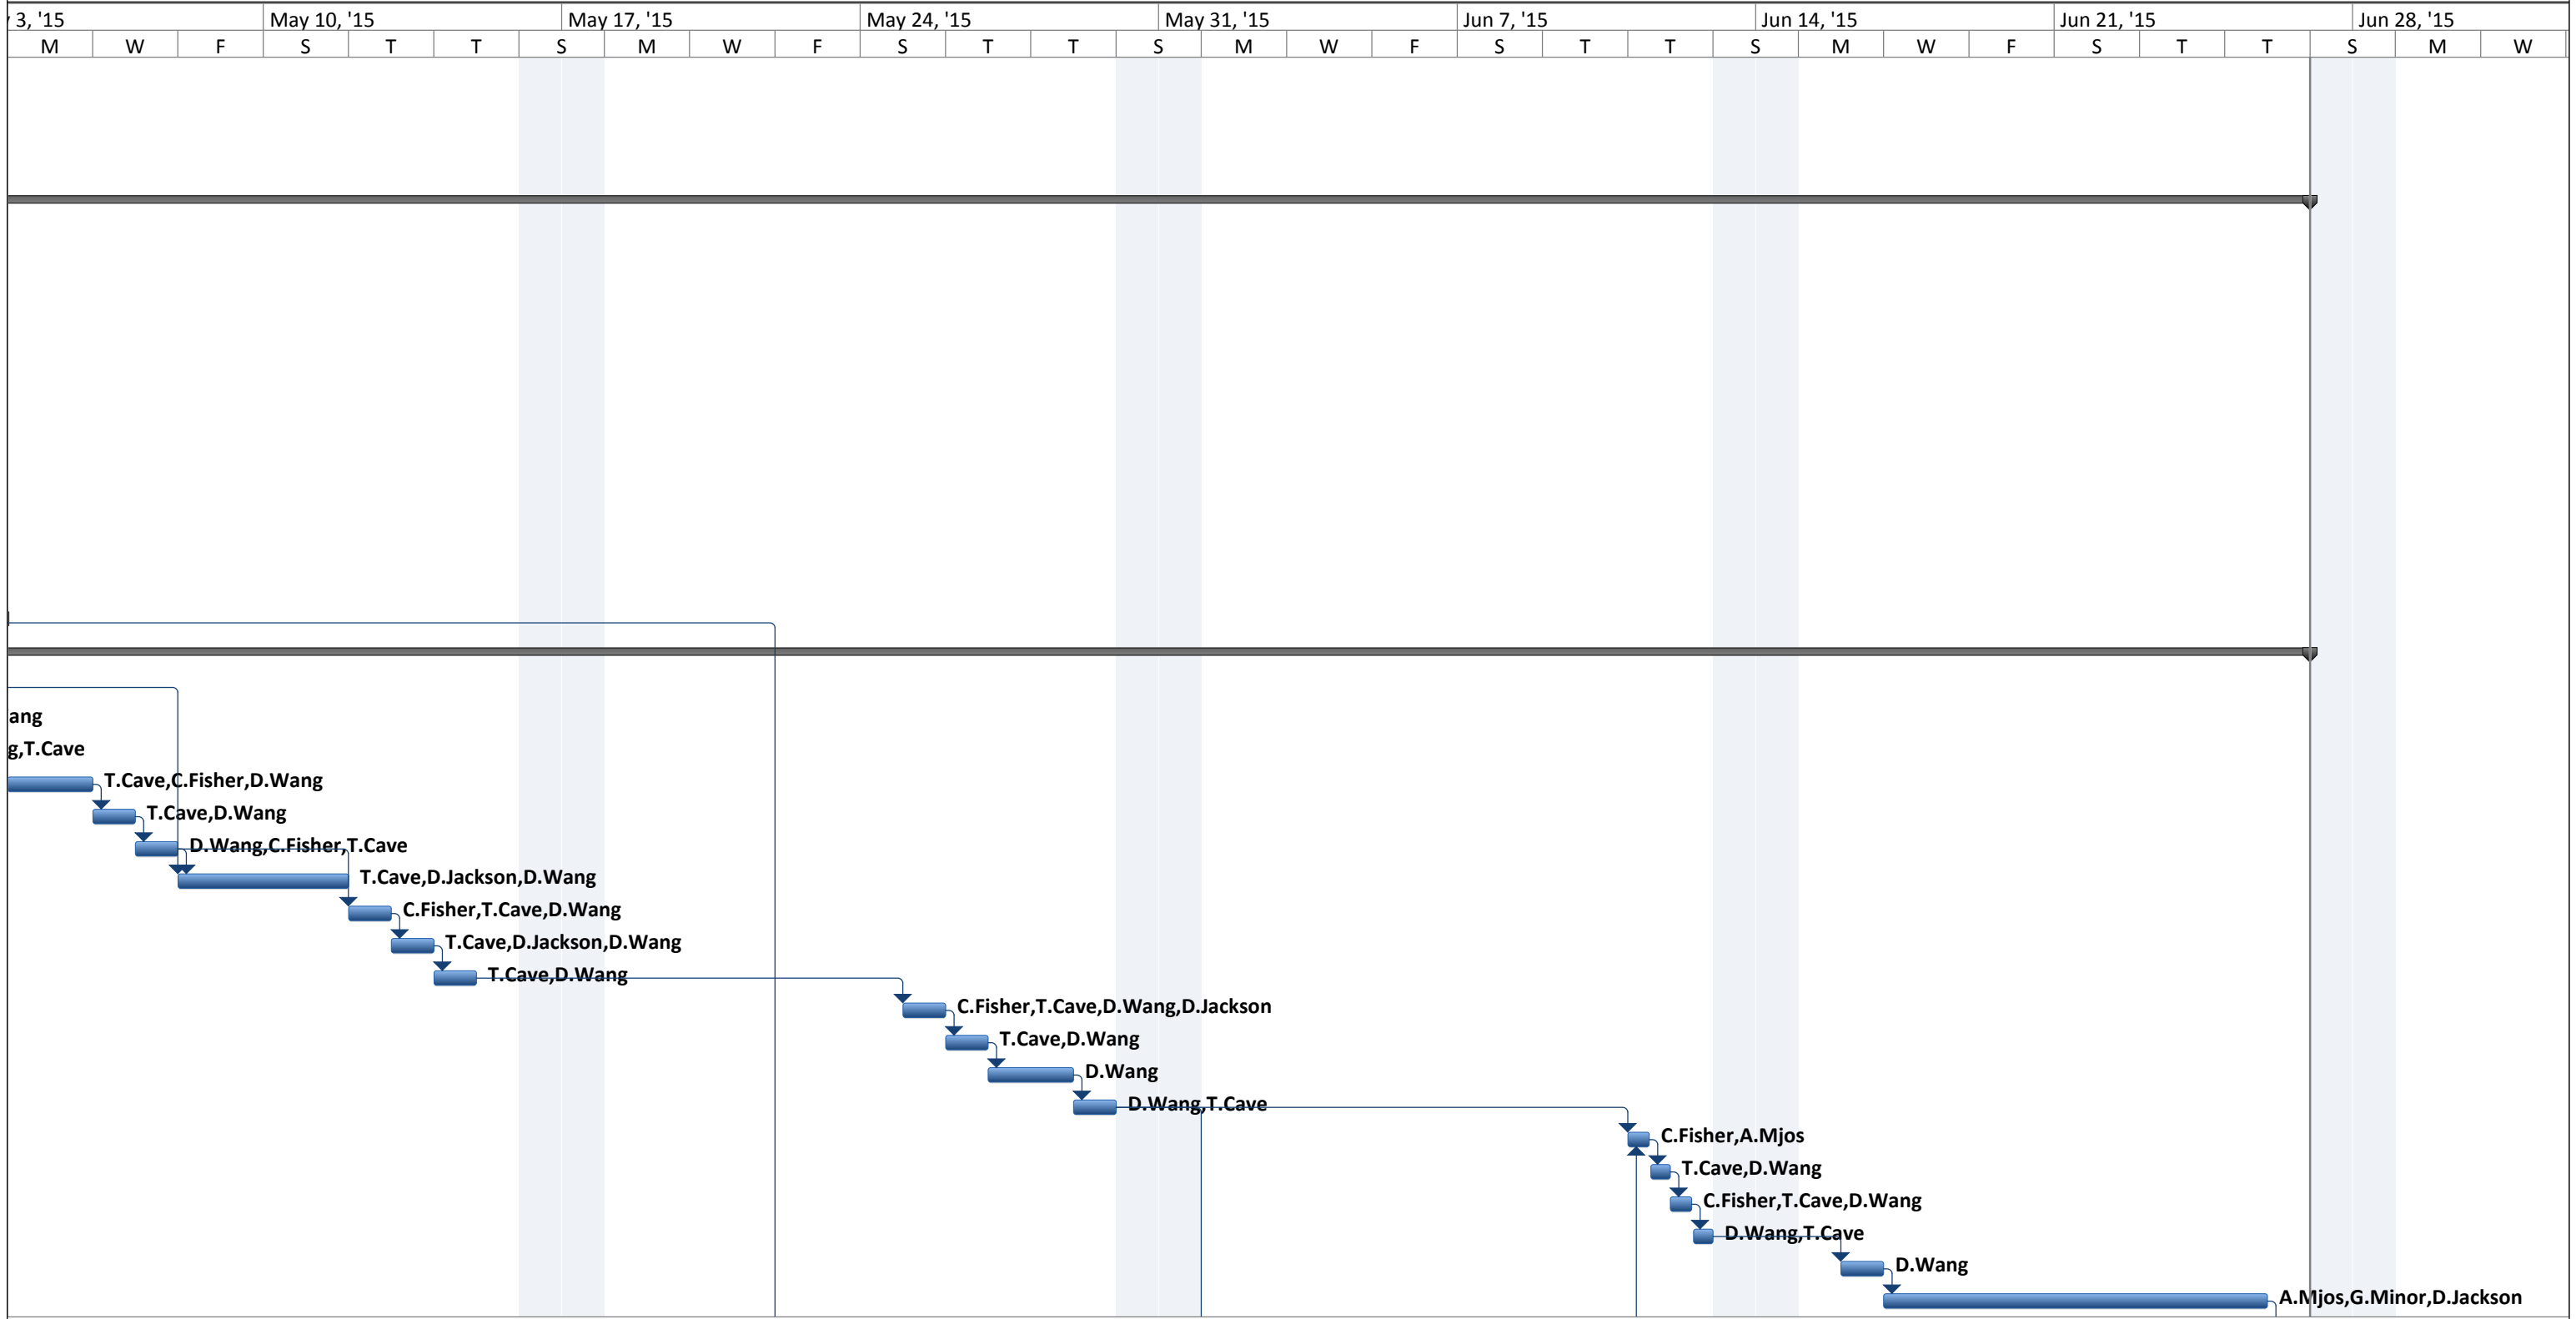

Project: Target Hall Scheduled Act Date: Mon 4/20/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

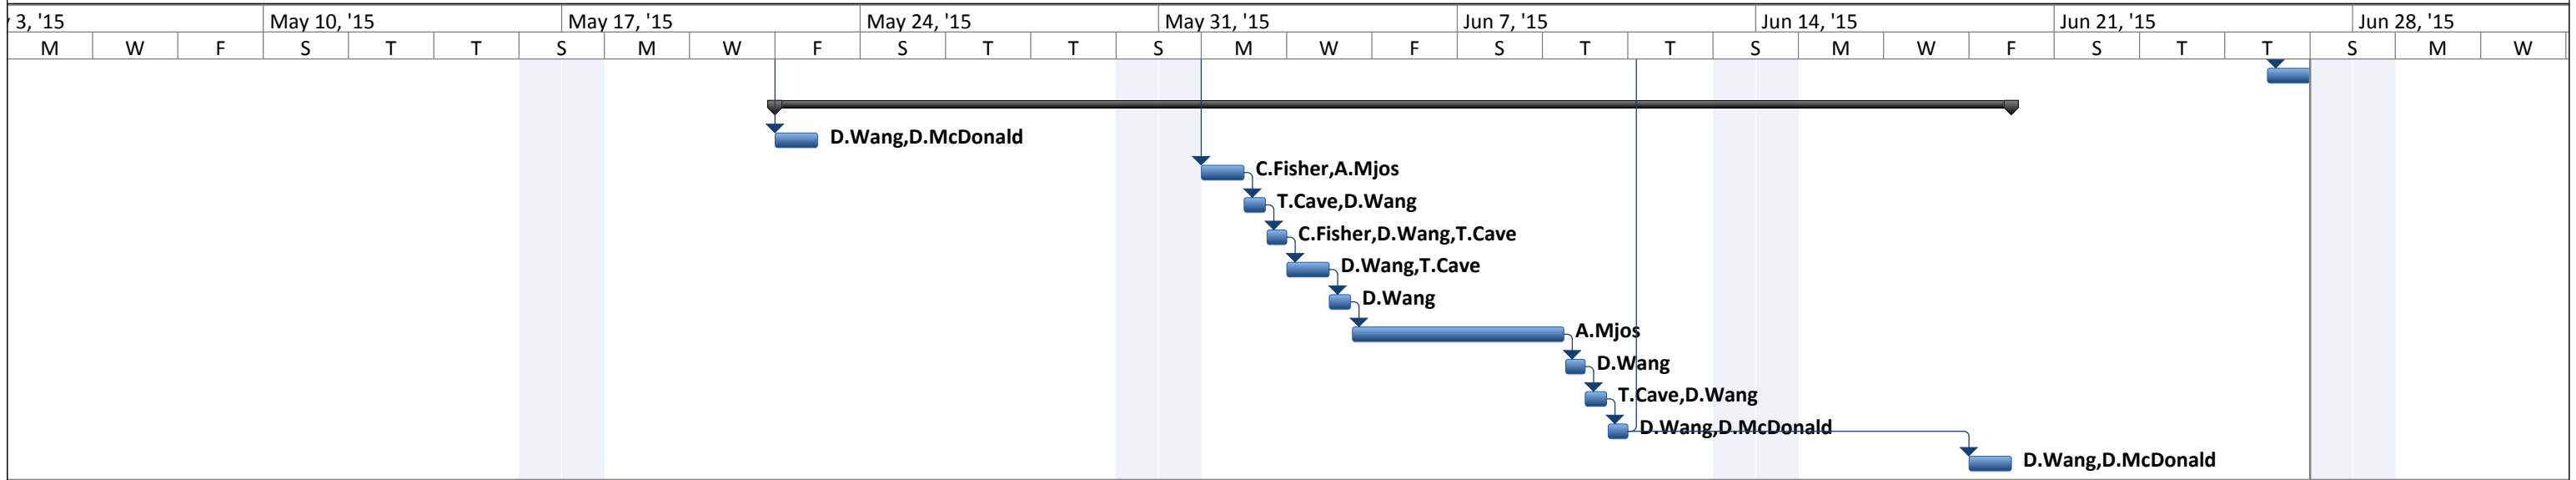

Project: Target Hall Scheduled Act Date: Mon 4/20/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
