

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	May					June				July	
							4/26	5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5
1	✓	TM4 Ta#45 ready for Beam at ITE	4 days	Tue 4/7/15	Fri 4/10/15												
2	✓	Grounding Test-ITW, ITE	1 day	Tue 4/7/15	Tue 4/7/15												
3	✓	Foot Anchors Grout-ITW, ITE Handrails	2.5 days	Wed 4/8/15	Fri 4/10/15	2											
4	✓	Shielding Blocks Move-ITW to ITE	0.5 days	Fri 4/10/15	Fri 4/10/15	3											
5		TM1-TM2-TM4 Target Hall Activities	55 days	Mon 4/13/15	Fri 6/26/15		[Summary Bar]										
6	✓	TM1 UCx Ready for Beam at ITW	8 days	Fri 4/17/15	Tue 4/28/15		[Summary Bar]										
7	✓	New Ucx Target in SHC/Cameras set up	0.2 days	Fri 4/17/15	Fri 4/17/15		[Summary Bar]										
8	✓	Moduel Move-TM1-Silo to SHC	0.2 days	Fri 4/17/15	Fri 4/17/15	7	[Summary Bar]										
9	✓	Ucx target install /Leak , Electrical Check at SHC	0.2 days	Fri 4/17/15	Fri 4/17/15	8	[Summary Bar]										
10	✓	Module Move- TM1 -SHC to CS	0.2 days	Fri 4/17/15	Fri 4/17/15	9	[Summary Bar]										
11	✓	TM1 Vacuum Connect at CS/ CS Pump Down	0.2 days	Fri 4/17/15	Fri 4/17/15	10	[Summary Bar]										
12	✓	Heium Pressure Test-TM1 HS line at CS	0.5 days	Mon 4/20/15	Mon 4/20/15	11	[Summary Bar]										
13	✓	TM1 Connect at CS/HV Cover Installed	0.5 days	Mon 4/20/15	Mon 4/20/15	12	[Summary Bar]										
14	✓	Module Conditioning-TM1 at CS	4.5 days	Tue 4/21/15	Mon 4/27/15	13	[Summary Bar]										
15	✓	Finish of Conditioning/Module Disconnect -TM1 at CS	0.5 days	Mon 4/27/15	Mon 4/27/15	14	[Summary Bar]										
16	✓	Argon Vent CS /ITW cameras Set up/Shield Plug Move from ITW	0.25 days	Tue 4/28/15	Tue 4/28/15	15	[Summary Bar]										
17	✓	Module Move -TM1-CS to ITW	0.25 days	Tue 4/28/15	Tue 4/28/15	16	[Summary Bar]										
18	✓	Module Connect-TM1 at ITW/Start of Turbopumps	0.5 days	Tue 4/28/15	Tue 4/28/15	17	[Summary Bar]										
19		TM2 Refurbishment Completion	55 days	Mon 4/13/15	Fri 6/26/15		[Summary Bar]										
20	✓	TM2 Top Service Cap Reconfiguration	3 days	Mon 4/13/15	Wed 4/15/15		[Summary Bar]										

Project: Target Hall Scheduled Act
Date: Mon 5/11/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	May					June			July			
							4/26	5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5	
21	✓	Module Move -TM2-Silo to ITW	1 day	Thu 4/30/15	Thu 4/30/15		T.Cave,D.Wang											
22	✓	TM2 Wiring Prepare/Work Area Set up in TH	1 day	Fri 5/1/15	Fri 5/1/15	21	D.Wang,T.Cave											
23	✓	TM2 Wiring - SHC & TM2 Service Cap	2 days	Mon 5/4/15	Tue 5/5/15	22	T.Cave,C.Fisher,D.Wang											
24		Module Move-TM2-SHC to CS	1 day	Fri 5/15/15	Fri 5/15/15		T.Cave,D.Wang											
25		Source Tray Install on Transfer Table/Transfer Source Tray into SHC	0.5 days	Tue 5/19/15	Tue 5/19/15		D.Wang,C.Fisher,T.Cave											
26		Remove Transfer table-SHC to TH/Clean up	0.5 days	Tue 5/19/15	Tue 5/19/15	25	C.Fisher,T.Cave,D.Wang											
27		Module Move- TM2 -CS to SHC	1 day	Wed 5/20/15	Wed 5/20/15	26	T.Cave,D.Wang											
28		Leak, Electrical Check-TM2 at SHC	1 day	Wed 5/27/15	Wed 5/27/15	27	C.Fisher,T.Cave,D.Wang,D.Jackson											
29		Module Move-TM2-SHC to CS/ Start of CS Pumps	1 day	Thu 5/28/15	Thu 5/28/15	28	T.Cave,D.Wang											
30		Helium Pressure Test on TM2 Water Lines at CS	0.5 days	Fri 5/29/15	Fri 5/29/15	29	D.Wang											
31		Module Move -TM2-CS to Silo	0.5 days	Fri 5/29/15	Fri 5/29/15	30	D.Wang,T.Cave											
32		TM2 Dummy Target Insert-SHC	0.5 days	Thu 6/11/15	Thu 6/11/15	31,49	C.Fisher,A.Mjos											
33		Module Move-TM2-Silo to SHC	0.5 days	Thu 6/11/15	Thu 6/11/15	32	T.Cave,D.Wang											
34		Dummy Target Install/Leak, Electrical Check	0.5 days	Fri 6/12/15	Fri 6/12/15	33	C.Fisher,T.Cave,D.Wang											
35		Module Move- TM2 -SHC to CS/Start of CS Pumps	0.5 days	Fri 6/12/15	Fri 6/12/15	34	D.Wang,T.Cave											
36		Helium Pressure Test -TM2 HS Line at CS/TM2 Connect at CS	1 day	Tue 6/16/15	Tue 6/16/15	35	D.Wang											
37		TM2 Test at CS	7 days	Wed 6/17/15	Thu 6/25/15	36	A.Mjos,G.Minor,D.Jackson											
38		TM2 Fully Operational/Complete TM2 Refurbishment	1 day	Fri 6/26/15	Fri 6/26/15	37												
39		TM4 HpSiC Ready for Beam at ITE	21 days	Fri 5/22/15	Fri 6/19/15		[Summary Bar]											

Project: Target Hall Scheduled Act Date: Mon 5/11/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	May							June				July		
							4/26	5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5			
							40		Shielding Blocks Move-ITE to ITW	1 day	Fri 5/22/15	Fri 5/22/15	18							
41		New HP SiC Target in SHC	1 day	Mon 6/1/15	Mon 6/1/15	31														
42		Cameras set up/Module Move-TM4 -ITE to SHC	0.5 days	Tue 6/2/15	Tue 6/2/15	41														
43		New SiC Target Install/Electrical,vacuum Check	0.5 days	Tue 6/2/15	Tue 6/2/15	42														
44		Module Move-TM4-SHC to CS/Start of CS Turbo Pumps	1 day	Wed 6/3/15	Wed 6/3/15	43														
45		Helium Pressure Test/Connect TM4 At CS/HV Cover on	0.5 days	Thu 6/4/15	Thu 6/4/15	44														
46		Module Conditioning-TM4 at CS	3 days	Thu 6/4/15	Tue 6/9/15	45														
47		Finish of Conditioning/Module Disconnect -TM4 at CS	0.5 days	Tue 6/9/15	Tue 6/9/15	46														
48		Module Move -TM4-CS to ITE	0.5 days	Wed 6/10/15	Wed 6/10/15	47														
49		Module Connect-TM4 at ITW/Start of ITE Turbopumps	0.5 days	Wed 6/10/15	Wed 6/10/15	48														
50		Shielding Blocks Move-ITW to ITE/ ITE Ready for Proton Beam	1 day	Fri 6/19/15	Fri 6/19/15	49														

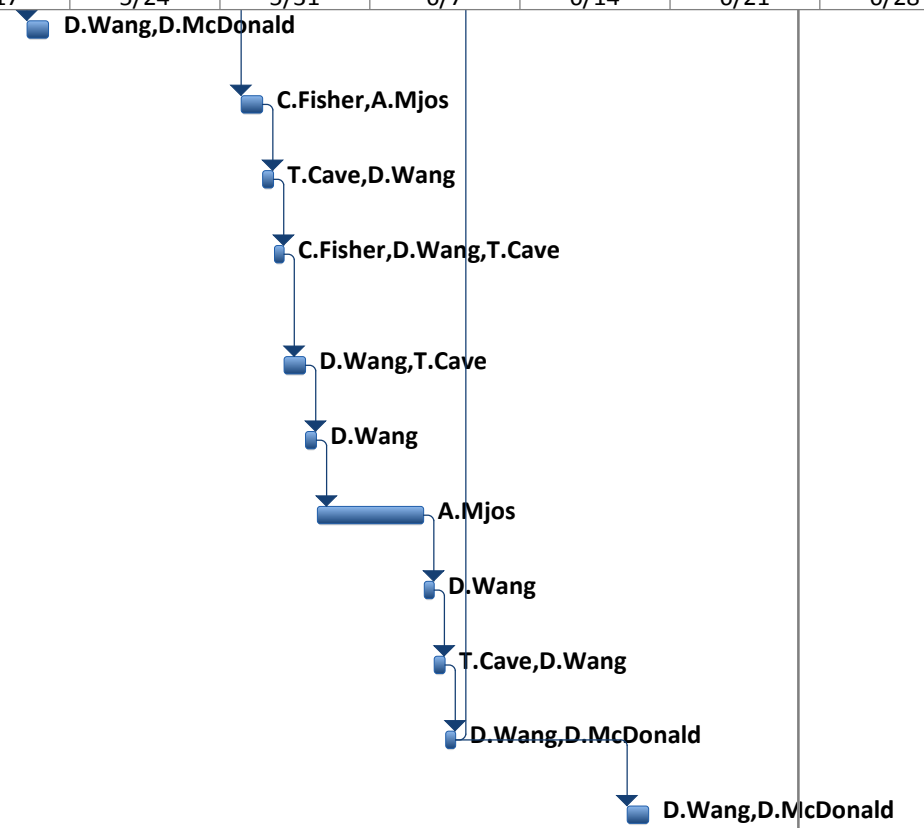

Project: Target Hall Scheduled Act
Date: Mon 5/11/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
