

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26


ID	Task Name	Duration	Start	May				June				July				
				5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5	7/12	7/19	
1	<b>TM4 Ta#45 ready for Beam at ITE</b>	4 days	Tue 4/7/15													
2	Grounding Test-ITW, ITE	1 day	Tue 4/7/15													
3	Foot Anchors Grout-ITW, ITE Handrails	2.5 days	Wed 4/8/15													
4	Shielding Blocks Move-ITW to ITE	0.5 days	Fri 4/10/15													
5	<b>TM1-TM2-TM4 Target Hall Activities</b>	61 days	Mon 4/13/15	[Summary Bar]												
6	<b>TM1 UCx Ready for Beam at ITW</b>	8 days	Fri 4/17/15													
7	New Ucx Target in SHC/Cameras set up	0.2 days	Fri 4/17/15													
8	Moduel Move-TM1-Silo to SHC	0.2 days	Fri 4/17/15													
9	Ucx target install /Leak , Electrical Check at SHC	0.2 days	Fri 4/17/15													
10	Module Move- TM1 -SHC to CS	0.2 days	Fri 4/17/15													
11	TM1 Vacuum Connect at CS/ CS Pump Down	0.2 days	Fri 4/17/15													
12	Heium Pressure Test-TM1 HS line at CS	0.5 days	Mon 4/20/15													
13	TM1 Connect at CS/HV Cover Installed	0.5 days	Mon 4/20/15													
14	Module Conditioning-TM1 at CS	4.5 days	Tue 4/21/15													
15	Finish of Conditioning/Module Disconnect -TM1 at CS	0.5 days	Mon 4/27/15													
16	Argon Vent CS /ITW cameras Set up/Shield Plug Move from ITW	0.25 days	Tue 4/28/15													
17	Module Move -TM1-CS to ITW	0.25 days	Tue 4/28/15													
18	Module Connect-TM1 at ITW/Start of Turbopumps	0.5 days	Tue 4/28/15													
19	<b>TM2 Refurbishment Completion</b>	61 days	Mon 4/13/15	[Summary Bar]												
20	TM2 Top Service Cap Reconfiguration	3 days	Mon 4/13/15													
21	Module Move -TM2-Silo to ITW	1 day	Thu 4/30/15													
22	TM2 Wiring Prepare/Work Area Set up in TH	1 day	Fri 5/1/15													
23	TM2 Wiring - SHC & TM2 Service Cap	2 days	Mon 5/4/15													
24	Module Move-TM2-SHC to CS	1 day	Mon 5/25/15													
25	TM2 wiring-TM2 at CS	2 days	Tue 5/26/15													
26	Module move-TM2 -CS to Silo	1 day	Thu 5/28/15													
27	Source Tray Install on Transfer Table/Transfer Source Tray into SHC	1 day	Thu 6/11/15													
28	Remove Transfer table-SHC to TH/Clean up	0.5 days	Fri 6/12/15													
29	Dummy Target Insert to SHC	0.5 days	Fri 6/12/15													
30	Module Move- TM2 -Silo to SHC	1 day	Mon 6/15/15													
31	Leak, Electrical Check-TM2 at SHC	1 day	Mon 6/22/15													
32	Module Move-TM2-SHC to CS/ Start of CS Pumps	1 day	Tue 6/23/15													
33	Helium Pressure Test -TM2 water lines at CS/TM2 Connect at CS	1 day	Wed 6/24/15													
34	TM2 Test at CS	7 days	Thu 6/25/15													
35	TM2 Fully Operational/Complete TM2 Refurbishment	1 day	Mon 7/6/15													
36	<b>TM4 HpSiC Ready for Beam at ITE</b>	21 days	Fri 5/22/15													
37	Shielding Blocks Move-ITE to ITW	1 day	Fri 5/22/15													
38	New HP SiC Target in SHC	1 day	Mon 6/1/15													
39	Cameras set up/Module Move-TM4 -ITE to SHC	0.5 days	Tue 6/2/15													

Project: Target Hall Scheduled Act  
Date: Tue 5/12/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

Target Hall Scheduled Activities 2015-04-07 to 2015 06-26

ID	Task Name	Duration	Start	June							July					
				5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5	7/12	7/19	
40	New SiC Target Install/Electrical,vacuum Check	0.5 days	Tue 6/2/15													
41	Module Move-TM4-SHC to CS/Start of CS Turbo Pumps	1 day	Wed 6/3/15													
42	Spent Target Move -HPTa-SHC to Storage Vault	0.5 days	Thu 6/4/15													
43	Helium Pressure Test/Connect TM4 At CS/HV Cover on	0.5 days	Thu 6/4/15													
44	Module Conditioning-TM4 at CS	2.5 days	Thu 6/4/15													
45	Finish of Conditioning/Module Disconnect -TM4 at CS	0.5 days	Tue 6/9/15													
46	Module Move -TM4-CS to ITE	0.5 days	Wed 6/10/15													
47	Module Connect-TM4 at ITW/Start of ITE Turbopumps	0.5 days	Wed 6/10/15													
48	Shielding Blocks Move-ITW to ITE/ ITE Ready for Proton Beam	1 day	Fri 6/19/15													

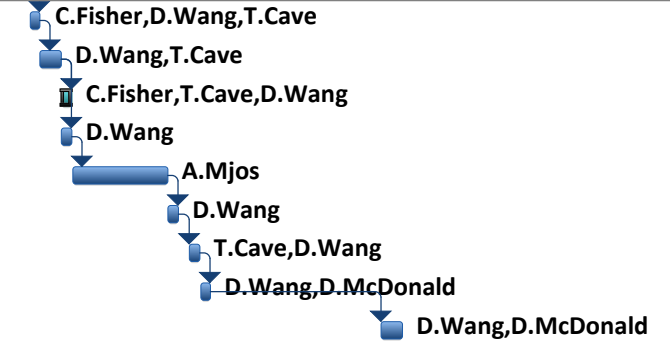

Project: Target Hall Scheduled Act Date: Tue 5/12/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
