Target Hall Scheduled Activities 2015-04-07 to 2015 08-19

ID	Task Mode	Task Name	Duration	Start	Finish
1		**TM4 Ta#45 ready for Beam at ITE**	**4 days**	**Tue 4/7/15**	**Fri 4/10/15**
5		**TM1-TM2-TM4 Target Hall Activities**	**107 days**	**Mon 4/13/15**	**Tue 9/8/15**
6		**TM1 UCx Ready for Beam at ITW**	**8 days**	**Fri 4/17/15**	**Tue 4/28/15**
19		**TM2 Refurbishment Completion**	**94 days**	**Mon 4/13/15**	**Thu 8/20/15**
20		TM2 Top Service Cap Reconfiguration	3 days	Mon 4/13/15	Wed 4/15/15
21		Module Move -TM2-Silo to ITW	1 day	Thu 4/30/15	Thu 4/30/15
22		TM2 Wiring Prepare/Work Area Set up in TH	1 day	Fri 5/1/15	Fri 5/1/15
23		TM2 Wiring - SHC & TM2 Service Cap	2 days	Mon 5/4/15	Tue 5/5/15
24		Module Move-TM2-SHC to CS	1 day	Wed 5/27/15	Wed 5/27/15
25		TM2 wiring-TM2 at CS	1 day	Thu 5/28/15	Thu 5/28/15
26		Module move-TM2 -CS to Silo	1 day	Fri 5/29/15	Fri 5/29/15
27		Source Tray Install on Transfer Table/Transfer Source Tray into SHC	1 day	Thu 6/11/15	Thu 6/11/15
28		Remove Transfer table-SHC to TH/Clean up	0.5 days	Fri 6/12/15	Fri 6/12/15
29		Module Move- TM2 -Silo to SHC	1 day	Mon 6/15/15	Mon 6/15/15
30		Leak, Electrical Check-TM2 at SHC	1 day	Wed 6/24/15	Wed 6/24/15
31		Module Move-TM2-SHC to CS/ Start of CS Pumps	1 day	Fri 6/26/15	Fri 6/26/15
32		Helium Pressure Test -TM2 water lines at CS/TM2 Connnect at CS	1 day	Mon 6/29/15	Mon 6/29/15
33		Module move-TM2- CS to SHC	1 day	Fri 7/3/15	Mon 7/6/15
34		Module Move-TM2-SHC to Silo	0.5 days	Thu 7/9/15	Thu 7/9/15
35		Module Move-TM1 -Silo-CS/ Start roughing CS	0.5 days	Thu 7/9/15	Thu 7/9/15
36		Start CS turbo-pumps /CS and TM 1 Pump down	1 day	Fri 7/10/15	Fri 7/10/15
37		Module Move TM1- CS to Silo	0.5 days	Mon 7/13/15	Mon 7/13/15
38		Dummy Target Insert into SHC	0.5 days	Mon 7/13/15	Mon 7/13/15
39		Module Move -TM2-Silo to SHC	1 day	Tue 7/14/15	Tue 7/14/15
40		TM2 Coil Line Leak Check/Electrical Check	1 day	Wed 7/15/15	Wed 7/15/15
41		Module Move-TM2-SHC to Silo	0.5 days	Fri 7/24/15	Fri 7/24/15
42		Module Move TM2- Silo to SHC	0.5 days	Thu 8/6/15	Thu 8/6/15
43		Module Move-TM2-SHC to CS	0.5 days	Thu 8/13/15	Thu 8/13/15
44		Module Connect-TM2 at CS/ Start of pumping	0.5 days	Thu 8/13/15	Thu 8/13/15
45		TM2 Test at CS with Dummy Target	4 days	Fri 8/14/15	Wed 8/19/15
46		Finish of TM2 TEST /Module Disconnect-TM2 at CS	0.5 days	Thu 8/20/15	Thu 8/20/15
47		Module Move TM2-CS to HC	0.5 days	Thu 8/20/15	Thu 8/20/15
48		**TM4 HpSiC Ready for Beam at ITE**	**21 days**	**Fri 5/22/15**	**Fri 6/19/15**
61		**TM1 Phase out/TM2 First Run Start in ITW**	**51 days**	**Tue 6/30/15**	**Tue 9/8/15**
62		Cameras Set up/Module Move-TM1 -ITW to SHC	0.5 days	Tue 6/30/15	Tue 6/30/15
63		Lp UCx Target Remove/ Electrical Check at SHC	0.5 days	Tue 6/30/15	Tue 6/30/15
64		Module Move- TM1 -SHC to Silo	0.5 days	Thu 7/2/15	Thu 7/2/15
65		Spent Target Move -Lp UCx-SHC to Storage Vault	0.5 days	Thu 7/2/15	Thu 7/2/15
66		Shielding Blocks Move- ITE to Storage Area	0.5 days	Fri 7/24/15	Fri 7/24/15
67		New Target in SHC for TM2	0.25 days	Wed 8/26/15	Wed 8/26/15
68		New Target Installation/ Electrical, Vacuum Check	0.25 days	Wed 8/26/15	Wed 8/26/15
69		Module Move -TM2-SHC to CS/Start of CS Pumps	0.5 days	Wed 8/26/15	Wed 8/26/15
70		Helium Pressure Test/ Conditioning TM2 at CS	3 days	Thu 8/27/15	Mon 8/31/15
71		Module Move TM2-CS to ITW	0.5 days	Tue 9/1/15	Tue 9/1/15
72		Module Connect-TM2 at ITW/Start of Turbo Pumps	0.5 days	Tue 9/1/15	Tue 9/1/15
73		Shielding Blocks Move- ITE to ITW/ ITW is Ready for Beam	1 day	Tue 9/8/15	Tue 9/8/15
74		**TM4 LpUcX Ready for Beam at ITE**	**10 days**	**Mon 7/27/15**	**Fri 8/7/15**
84		**Spent Target Assay**	**7 days**	**Fri 7/31/15**	**Mon 8/10/15**

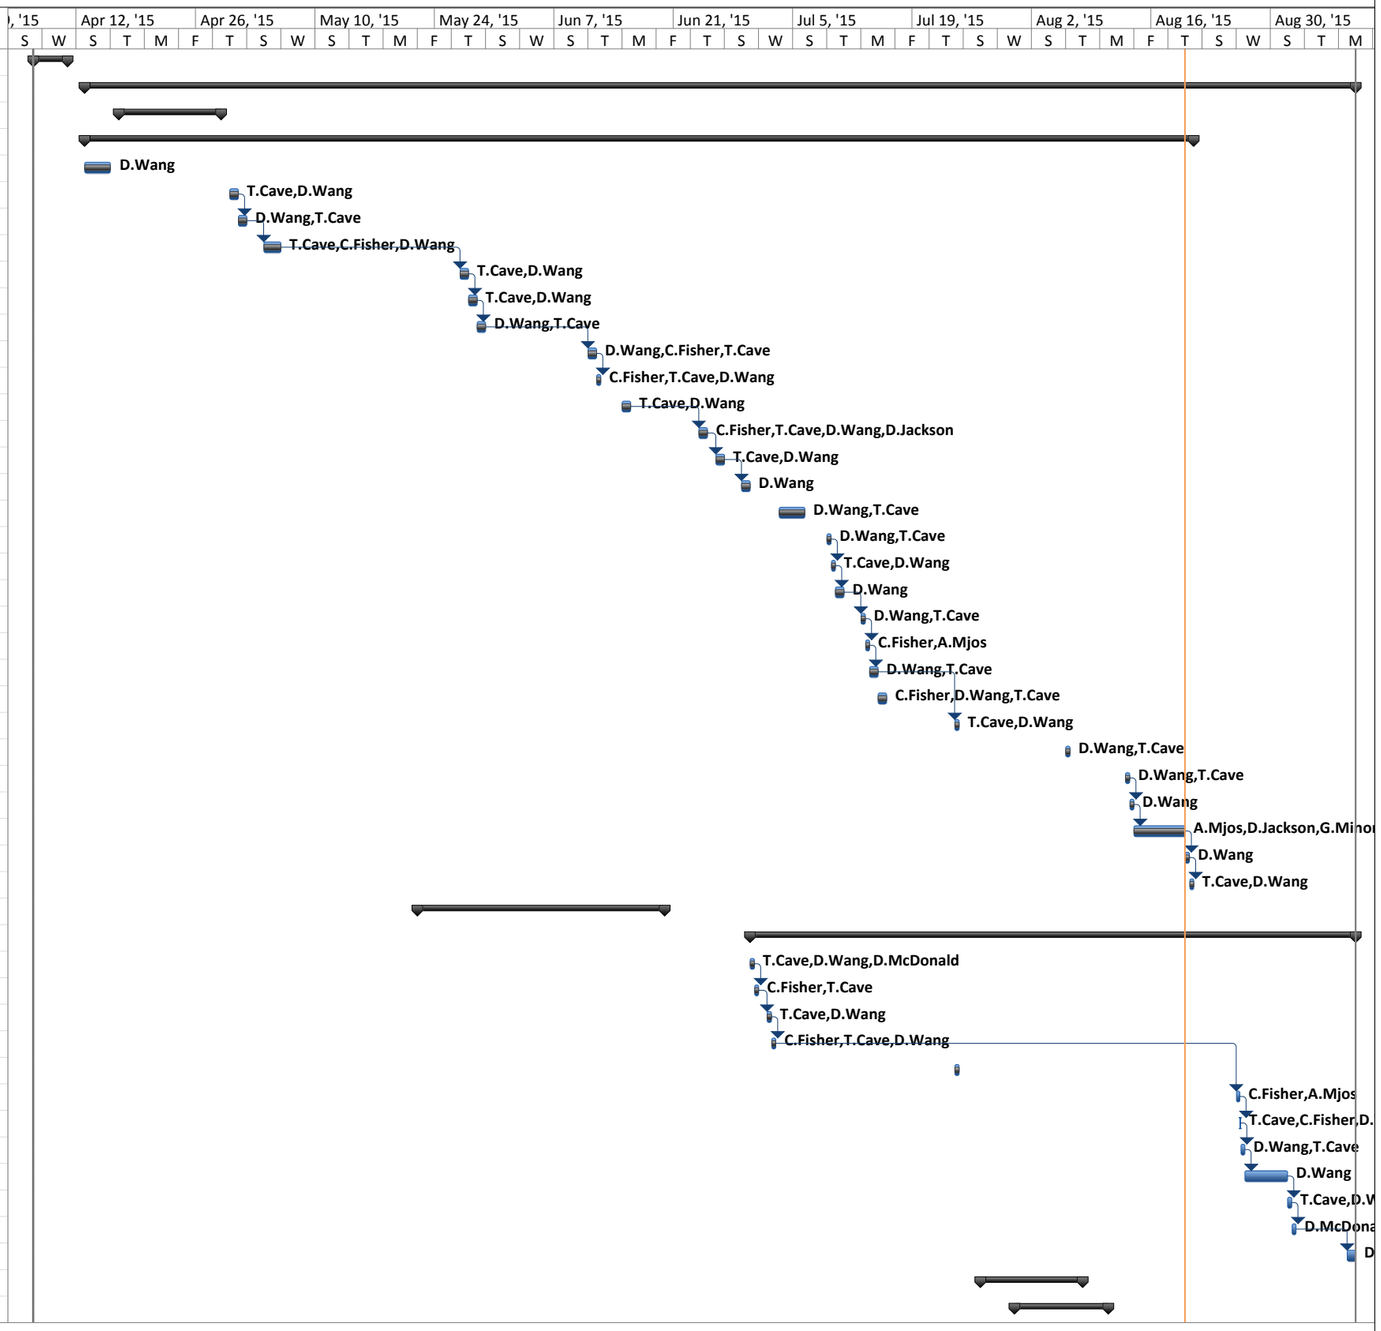

Project: Target Hall Scheduled Act
Date: Thu 8/20/15

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress
