Target Hall schedule from Sep 09th 2015 to Dec 30th 2015

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**TM1 Window Leak Investigation and Repairing -Stage 1**	**5.5 days**	**Wed 9/9/15**	**Wed 9/16/15**		
5		**TM4 with HpTa Ready for Beam in ITE**	**12 days**	**Mon 9/21/15**	**Tue 10/6/15**		
6		Cameras Set up/Module Disconnect -TM4 in ITE	0.25 days	Mon 9/21/15	Mon 9/21/15		T.Cave,D.Wang,D.M
7		HpTa Target Insert into SHC	0.25 days	Mon 9/21/15	Mon 9/21/15	6	A.Mjos,C.Fisher
8		Module Move -TM4- ITE to SHC	0.25 days	Mon 9/21/15	Mon 9/21/15	7	D.Wang,T.Cave
9		HpTa Target Installation/Leak, Electrical Check	0.25 days	Mon 9/21/15	Mon 9/21/15	8	C.Fisher,D.Wang,T.C
10		Module Move-TM4- SHC to CS	0.5 days	Tue 9/22/15	Tue 9/22/15	9	T.Cave,D.Wang
11		Module Connect- TM4 at CS/ Start of CS Pumps	0.5 days	Tue 9/22/15	Tue 9/22/15	10	D.Wang,D.McDonald
12		Spent Target Move-Ucx- SHC to storage Vault	0.5 days	Wed 9/23/15	Wed 9/23/15	11	C.Fisher,D.Wang,T.C
13		Helium Pressure Test/ TM4 Conditioning at CS	3.5 days	Wed 9/23/15	Mon 9/28/15	11	D.Wang,A.Mjos
14		Module Disconnect-TM4 at CS/Venting	0.25 days	Tue 9/29/15	Tue 9/29/15	13	D.Wang
15		Module Move -TM4- CS to ITE	0.25 days	Tue 9/29/15	Tue 9/29/15	14	T.Cave,D.Wang
16		Module Connect- TM4 in ITE/Start of Pumps	0.5 days	Tue 9/29/15	Tue 9/29/15	15	D.McDonald,D.Wang
17		Shielding Blocks Transfer -ITW to ITE	1 day	Tue 10/6/15	Tue 10/6/15	16	D.McDonald,D.Wang
18		**TM2 with HpSiC Ready for Beam in ITW**	**23 days**	**Wed 10/14/15**	**Fri 11/13/15**		
19		Cameras Set up/Module Disconnect-TM2 in ITW	0.25 days	Wed 10/14/15	Wed 10/14/15	17	D.Wang,W.Paley,D.M
20		HpSiC Target Insert into SHC	0.25 days	Wed 10/14/15	Wed 10/14/15	19	A.Mjos,C.Fisher
21		Module Move-TM2- ITW to SHC	0.25 days	Wed 10/14/15	Wed 10/14/15	20	D.Wang,W.Paley
22		Hp SiC Target Installation/Leak, Electrical Check	0.25 days	Wed 10/14/15	Wed 10/14/15	21	D.Wang,C.Fisher,D.M
23		New Anode Cable installation on TM2 Source Tray	0.5 days	Thu 10/15/15	Thu 10/15/15	22	C.Fisher,A.Mjos
24		Module Move -TM2- SHC to ITW	0.25 days	Tue 10/20/15	Tue 10/20/15		D.McDonald,T.Cave
25		Module Connect -TM2 in ITW / Start of Turbo Pumps	0.5 days	Tue 10/20/15	Tue 10/20/15	24	D.McDonald,A.Mjos
26		Spent Target Move -ZrC#7 -SHC to Storage Vault	1 day	Wed 10/21/15	Wed 10/21/15	24	C.Fisher,T.Cave
27		Shielding Blocks transfer - ITE to ITW	1 day	Fri 11/13/15	Fri 11/13/15	25	M.Dalla Valle,W.Pale
28		**TM4 with UCx Ready for Beam in ITE**	**10 days**	**Tue 11/24/15**	**Mon 12/7/15**		
29		Cameras Set up/Module Disconnect -TM4 in ITE	0.2 days	Tue 11/24/15	Tue 11/24/15	27	T.Cave,D.Wang
30		LpUCx Target Insert into SHC	0.2 days	Tue 11/24/15	Tue 11/24/15	29	A.Mjos,C.Fisher
31		Module Move -TM4-ITE to SHC	0.2 days	Tue 11/24/15	Tue 11/24/15	30	D.Wang
32		LpUCx Target Installation/Leak, Electrical Check	0.2 days	Tue 11/24/15	Tue 11/24/15	31	D.Wang,T.Cave
33		Module Move-TM4- SHC to CS/ Start of Pumps	0.2 days	Tue 11/24/15	Tue 11/24/15	32	D.Wang,T.Cave
34		Helium Pressure Test/Module Connect-TM4 at CS	0.5 days	Wed 11/25/15	Wed 11/25/15	33	D.Wang
35		TM4 Conditioning at CS	3.5 days	Wed 11/25/15	Mon 11/30/15	34	A.Mjos
36		Spent Target Move- HpTa- SHC to Storage Vault	1 day	Thu 11/26/15	Thu 11/26/15	33	C.Fisher,D.Wang,T.C
37		Module Disconnect- TM4 at CS/ Argon Venting CS	0.25 days	Tue 12/1/15	Tue 12/1/15	35	D.Wang
38		Module Move -TM4- CS to ITE	0.25 days	Tue 12/1/15	Tue 12/1/15	37	D.Wang,T.Cave
39		Module Connect -TM4 in ITE/ Start of Turbo-Pumps	0.5 days	Tue 12/1/15	Tue 12/1/15	38	D.Wang
40		Sheilding Blocks Transfer -ITW to ITE	1 day	Mon 12/7/15	Mon 12/7/15	39	D.Wang
41		**TM3 Evaluation at CS**	**8 days**	**Thu 11/5/15**	**Mon 11/16/15**		
42		Module Move-TM3 - Silo to CS	1 day	Thu 11/5/15	Fri 11/6/15		D.Wang,T.Cave
43		TM3 TP2 Replacement, Opened panel o-rings Replacement	0.25 days	Fri 11/6/15	Fri 11/6/15	42	D.Wang,A. Laxdal
44		Start of TM3 Vacuum Pumps at CS	0.5 days	Fri 11/6/15	Fri 11/6/15	43	D.Wang,A.Mjos
45		Leak Check/Helium Pressure, Air to Vacuum	0.5 days	Mon 11/9/15	Mon 11/9/15	44	A. Laxdal,D.Wang,A.
46		High Current Cables Installation/Start of CS Water Pumps	0.5 days	Mon 11/9/15	Mon 11/9/15	45	D.Wang,A. Laxdal
47		HV and other TM3 tests	4 days	Tue 11/10/15	Fri 11/13/15	46	A.Mjos,A. Laxdal
48		Module Move -TM3 - CS to Silo	1 day	Mon 11/16/15	Mon 11/16/15	47	D.Wang,T.Cave
49		**SHC clean up**	**5 days**	**Tue 11/17/15**	**Mon 11/23/15**		
50		Final Preparations for Cell Entry/Drum Waste Removal	1 day	Tue 11/17/15	Tue 11/17/15		C.Fisher,D.Wang
51		Drum Lower into Hot Cell/ Cell Entry	0.5 days	Wed 11/18/15	Wed 11/18/15	50	D.Wang,C.Fisher
52		Drum Filled with Waste / Crane out of Cell to B2 by Vault	0.5 days	Wed 11/18/15	Wed 11/18/15	51	C.Fisher,D.Wang
53		RPG Swipe Drum/ Drum Lowered into North Hot Cell	1 day	Thu 11/19/15	Thu 11/19/15	52	RPG,D.Wang
54		Second Drum Lower into Hot Cell/ Cell Entry	0.25 days	Mon 11/23/15	Mon 11/23/15		C.Fisher,D.Wang,T.C
55		Second Drum Filled with Waste/Crane out of Cell to B2	0.25 days	Mon 11/23/15	Mon 11/23/15	54	C.Fisher,D.Wang,T.C
56		RGP Swipe 2# Drum/Decon Drum/Drum Lowered into NHC	0.5 days	Mon 11/23/15	Mon 11/23/15	55	C.Fisher,D.Wang,RP

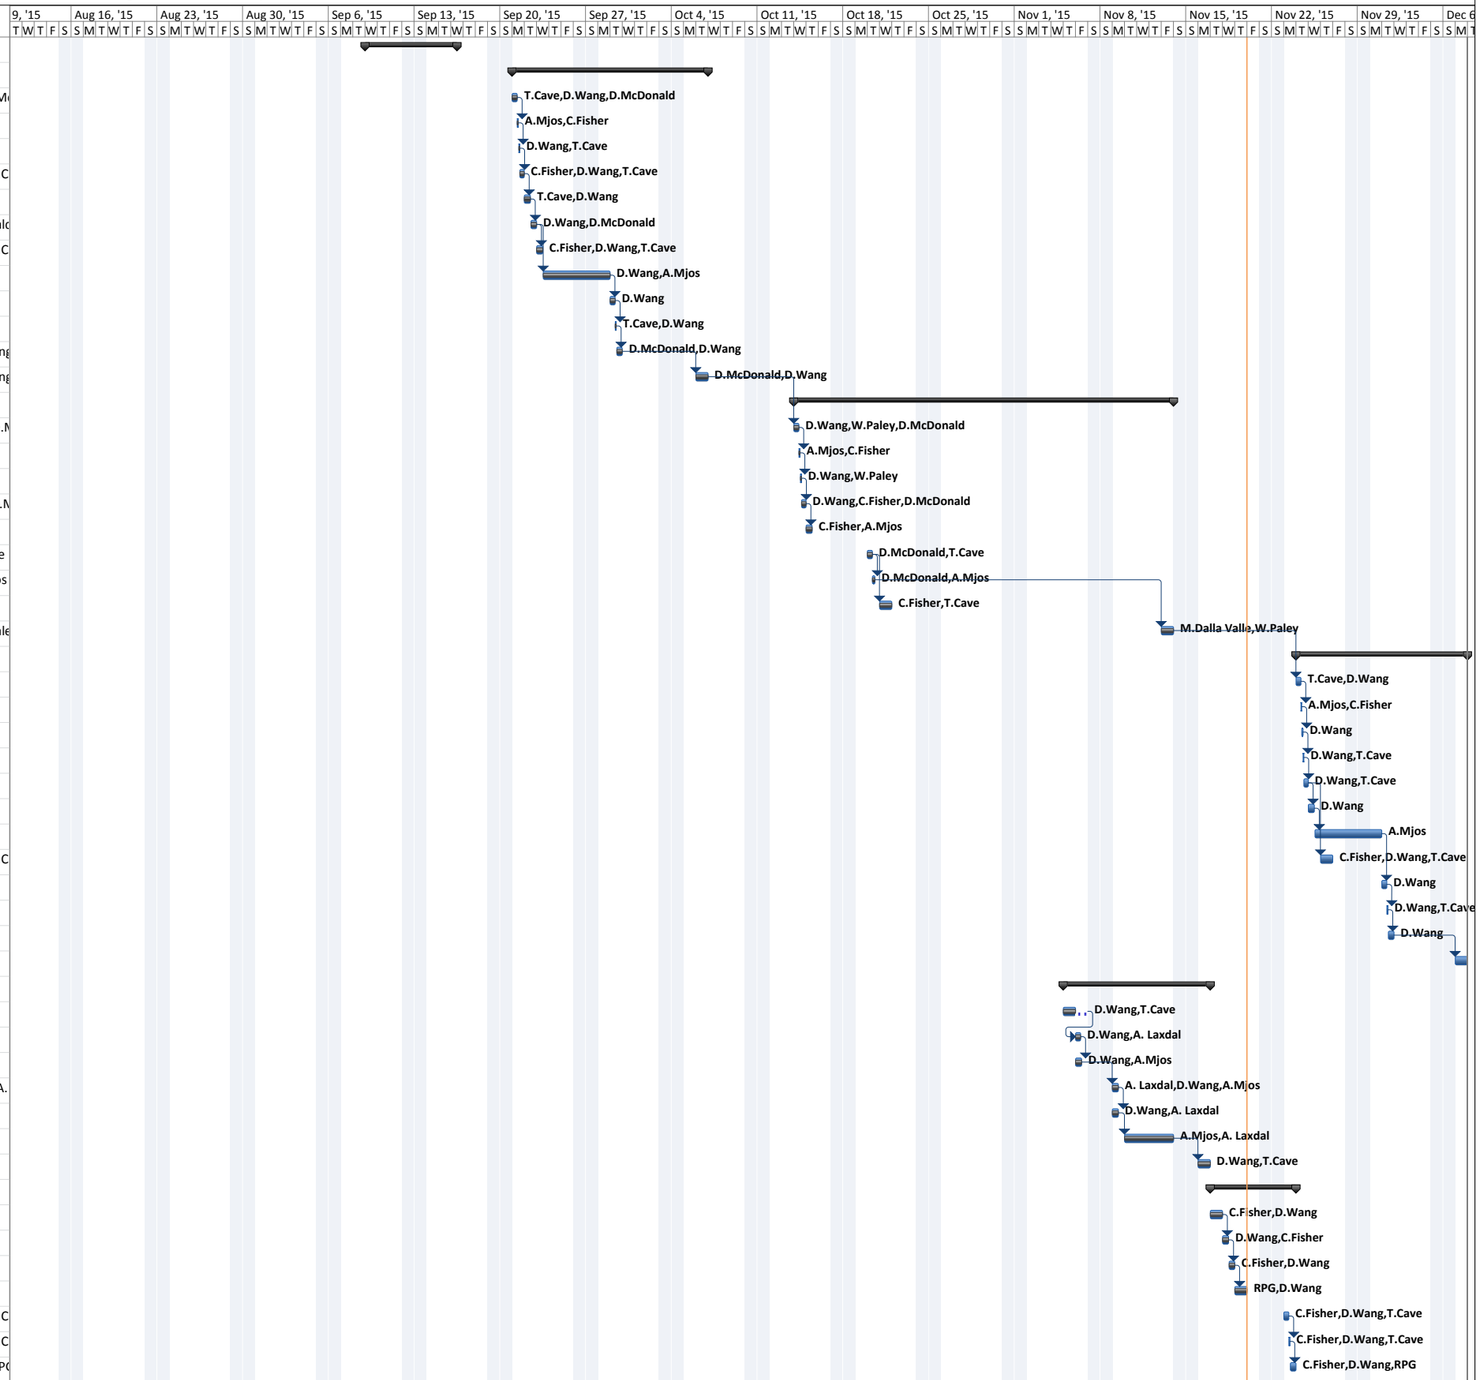

Project: Target Hall Scheduled Act
Date: Fri 11/20/15

Task | Milestone | Project Summary | External Milestone | Inactive Milestone | Manual Task | Manual Summary Rollup | Start-only | Deadline
Split | Summary | External Tasks | Inactive Task | Inactive Summary | Duration-only | Manual Summary | Finish-only | Progress
