Target Hall schedule from Sep 09th 2015 to Dec 30th 2015

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**TM1 Window Leak Investigation and Repairing -Stage 1**	**5.5 days**	**Wed 9/9/15**	**Wed 9/16/15**		
5	**TM4 with HpTa Ready for Beam in ITE**	**12 days**	**Mon 9/21/15**	**Tue 10/6/15**		
6	Cameras Set up/Module Disconnect -TM4 in ITE	0.25 days	Mon 9/21/15	Mon 9/21/15		T.Cave,D.Wang,D.M
7	HpTa Target Insert into SHC	0.25 days	Mon 9/21/15	Mon 9/21/15	6	A.Mjos,C.Fisher
8	Module Move -TM4- ITE to SHC	0.25 days	Mon 9/21/15	Mon 9/21/15	7	D.Wang,T.Cave
9	HpTa Target Installation/Leak, Electrical Check	0.25 days	Mon 9/21/15	Mon 9/21/15	8	C.Fisher,D.Wang,T.C
10	Module Move-TM4- SHC to CS	0.5 days	Tue 9/22/15	Tue 9/22/15	9	T.Cave,D.Wang
11	Module Connect- TM4 at CS/ Start of CS Pumps	0.5 days	Tue 9/22/15	Tue 9/22/15	10	D.Wang,D.McDonal
12	Spent Target Move-Ucx- SHC to storage Vault	0.5 days	Wed 9/23/15	Wed 9/23/15	11	C.Fisher,D.Wang,T.C
13	Helium Pressure Test/ TM4 Conditioning at CS	3.5 days	Wed 9/23/15	Mon 9/28/15	11	D.Wang,A.Mjos
14	Module Disconnect-TM4 at CS/Venting	0.25 days	Tue 9/29/15	Tue 9/29/15	13	D.Wang
15	Module Move -TM4- CS to ITE	0.25 days	Tue 9/29/15	Tue 9/29/15	14	T.Cave,D.Wang
16	Module Connect- TM4 in ITE/Start of Pumps	0.5 days	Tue 9/29/15	Tue 9/29/15	15	D.McDonald,D.Wang
17	Shielding Blocks Transfer -ITW to ITE	1 day	Tue 10/6/15	Tue 10/6/15	16	D.McDonald,D.Wang
18	**TM2 with HpSiC Ready for Beam in ITW**	**23 days**	**Wed 10/14/15**	**Fri 11/13/15**		
19	Cameras Set up/Module Disconnect-TM2 in ITW	0.25 days	Wed 10/14/15	Wed 10/14/15	17	D.Wang,W.Paley,D.M
20	HpSiC Target Insert into SHC	0.25 days	Wed 10/14/15	Wed 10/14/15	19	A.Mjos,C.Fisher
21	Module Move-TM2- ITW to SHC	0.25 days	Wed 10/14/15	Wed 10/14/15	20	D.Wang,W.Paley
22	Hp SiC Target Installation/Leak, Electrical Check	0.25 days	Wed 10/14/15	Wed 10/14/15	21	D.Wang,C.Fisher,D.M
23	New Anode Cable installation on TM2 Source Tray	0.5 days	Thu 10/15/15	Thu 10/15/15	22	C.Fisher,A.Mjos
24	Module Move -TM2- SHC to ITW	0.25 days	Tue 10/20/15	Tue 10/20/15		D.McDonald,T.Cave
25	Module Connect -TM2 in ITW / Start of Turbo Pumps	0.5 days	Tue 10/20/15	Tue 10/20/15	24	D.McDonald,A.Mjos
26	Spent Target Move -ZrC#7 -SHC to Storage Vault	1 day	Wed 10/21/15	Wed 10/21/15	24	C.Fisher,T.Cave
27	Shielding Blocks transfer - ITE to ITW	1 day	Fri 11/13/15	Fri 11/13/15	25	M.Dalla Valle,W.Pale
28	**TM4 with UCx Ready for Beam in ITE**	**10 days**	**Tue 11/24/15**	**Mon 12/7/15**		
29	Cameras Set up/Module Disconnect -TM4 in ITE	0.2 days	Tue 11/24/15	Tue 11/24/15	27	T.Cave,D.Wang
30	LpUCx Target Insert into SHC	0.2 days	Tue 11/24/15	Tue 11/24/15	29	A.Mjos,C.Fisher
31	Module Move -TM4-ITE to SHC	0.2 days	Tue 11/24/15	Tue 11/24/15	30	D.Wang
32	LpUCx Target Installation/Leak, Electrical Check	0.2 days	Tue 11/24/15	Tue 11/24/15	31	D.Wang,T.Cave
33	Module Move-TM4- SHC to CS/ Start of Pumps	0.2 days	Tue 11/24/15	Tue 11/24/15	32	D.Wang,T.Cave
34	Helium Pressure Test/Module Connect-TM4 at CS	0.5 days	Wed 11/25/15	Wed 11/25/15	33	D.Wang
35	TM4 Conditioning at CS	3.5 days	Wed 11/25/15	Mon 11/30/15	34	A.Mjos
36	Spent Target Move- HpTa- SHC to Storage Vault	1 day	Thu 11/26/15	Thu 11/26/15	33	C.Fisher,D.Wang,T.C
37	Module Disconnect- TM4 at CS/ Argon Venting CS	0.25 days	Tue 12/1/15	Tue 12/1/15	35	D.Wang
38	Module Move -TM4- CS to ITE	0.25 days	Tue 12/1/15	Tue 12/1/15	37	D.Wang,T.Cave
39	Module Connect -TM4 in ITE/ Start of Turbo-Pumps	0.5 days	Tue 12/1/15	Tue 12/1/15	38	D.Wang
40	Sheilding Blocks Transfer -ITW to ITE	1 day	Mon 12/7/15	Mon 12/7/15	39	D.Wang
41	**TM3 Evaluation at CS**	**8 days**	**Thu 11/5/15**	**Mon 11/16/15**		
49	**SHC clean up**	**12.5 days**	**Tue 11/17/15**	**Thu 12/3/15**		

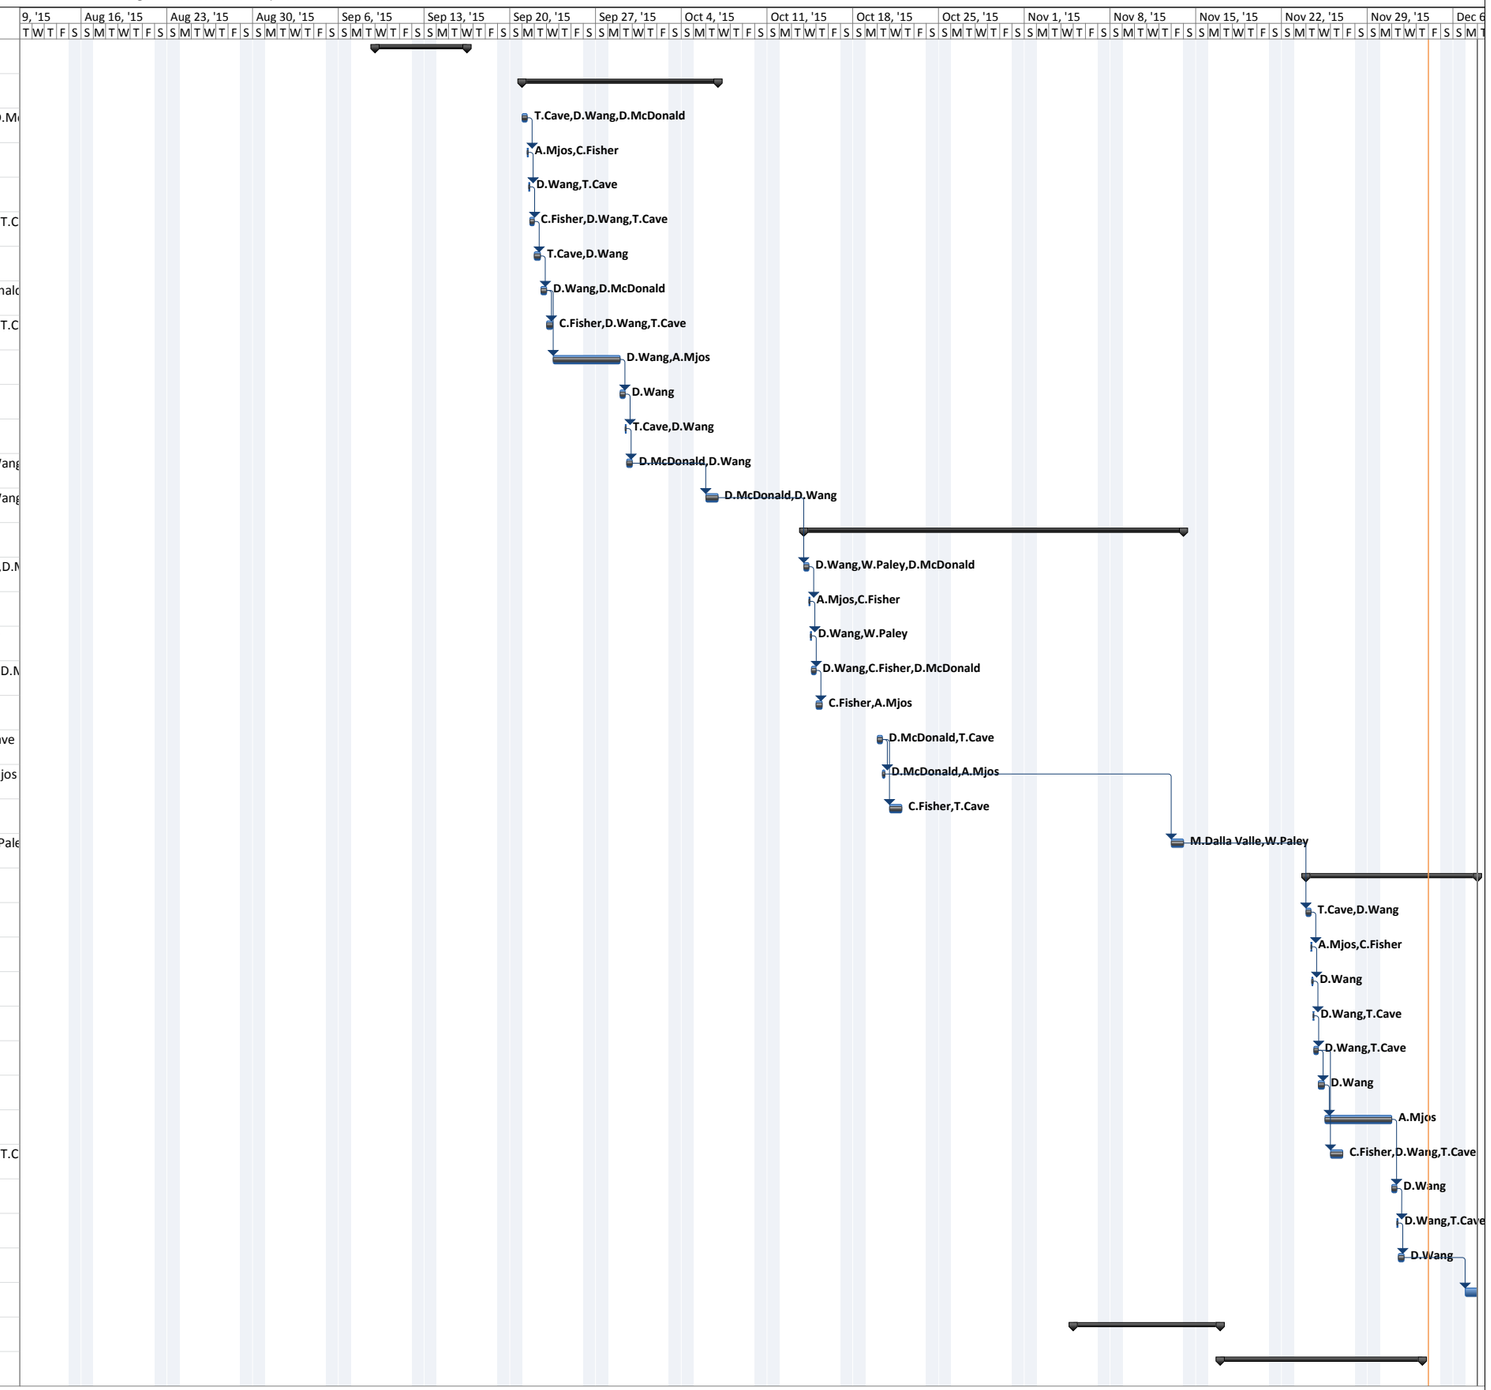

Project: Target Hall Scheduled Act
Date: Fri 12/4/15

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
