2016 WINTER SHUT DOWN TARGET HALL SCHEDULE

ID	Task Mode	Task Name	Duration	Start
1		**ITW flow and temperature senors update**	**3 days**	**Mon 2/22/16**
2		New flow senors assembly installation in ITW	2 days	Mon 2/22/16
3		new cables installation	1 day	Wed 2/24/16
4		**Shut Down Leak Check - Target Stations and Modules**	**4 days**	**Thu 2/25/16**
5		Module Disconnection-TM2/ITW	1 day	Thu 2/25/16
6		ITW and TM2 Vacuum Leak Check	1 day	Fri 2/26/16
7		Shielding Blocks Move- ITE to Storage Area	0.5 days	Mon 2/29/16
8		Module Disconnection-TM4-ITE	0.5 days	Mon 2/29/16
9		ITE and TM4 Vacuum leak Check	1 day	Tue 3/1/16
10		**ISAC Spent targets Shipment**	**2 days**	**Thu 2/18/16**
11		F308s Move- Ante Room to Target Hall	0.5 days	Thu 2/18/16
12		Working area Set up	0.5 days	Thu 2/18/16
13		Speant Targets Transfer- Mini Storage to F308s	0.5 days	Fri 2/19/16
14		F308s Move- Target Hall to Ante Room	0.5 days	Fri 2/19/16
15		**TM2 with New Target to ITW**	**10 days**	**Wed 3/2/16**
16		New Target Insert into SHC	0.25 days	Wed 3/2/16
17		Module Move -TM2- ITW to SHC	0.25 days	Wed 3/2/16
18		Target Removal and Electrical Check	0.5 days	Wed 3/2/16
19		New Target Installation	0.5 days	Thu 3/3/16
20		TM2 with New Target Leak and Electrical Check- SHC	0.5 days	Thu 3/3/16
21		Module Move -TM2-SHC to TCS	0.5 days	Fri 3/4/16
22		Module Connection- TM2 -TCS/Start of Pumps	0.5 days	Fri 3/4/16
23		Spent Target Move	1 day	Mon 3/14/16
24		Module Disconnection-TM2-TCS	0.25 days	Tue 3/15/16
25		Module Move-TM2- TCS to ITW	0.25 days	Tue 3/15/16
26		Module Connection-TM2-ITW/ Start of Pumps	0.5 days	Tue 3/15/16
27		**TM4 with New Target to ITE**	**3 days**	**Wed 3/16/16**
28		New Target Insert into SHC	0.25 days	Wed 3/16/16
29		Module Move -TM4-ITE to SHC	0.25 days	Wed 3/16/16
30		Target Removal and Electrical Check	0.25 days	Wed 3/16/16
31		New Target Installation	0.25 days	Wed 3/16/16
32		Leak Check and Electrical Check	0.5 days	Thu 3/17/16
33		Module Move -TM4-SHC to ITE	0.5 days	Thu 3/17/16
34		Module Connection- TM4 -ITE/ Start of Pumps	0.5 days	Fri 3/18/16
35		Spent Target Move	0.5 days	Fri 3/18/16
36		TM3 Refurbishment	30 days	Mon 3/21/16

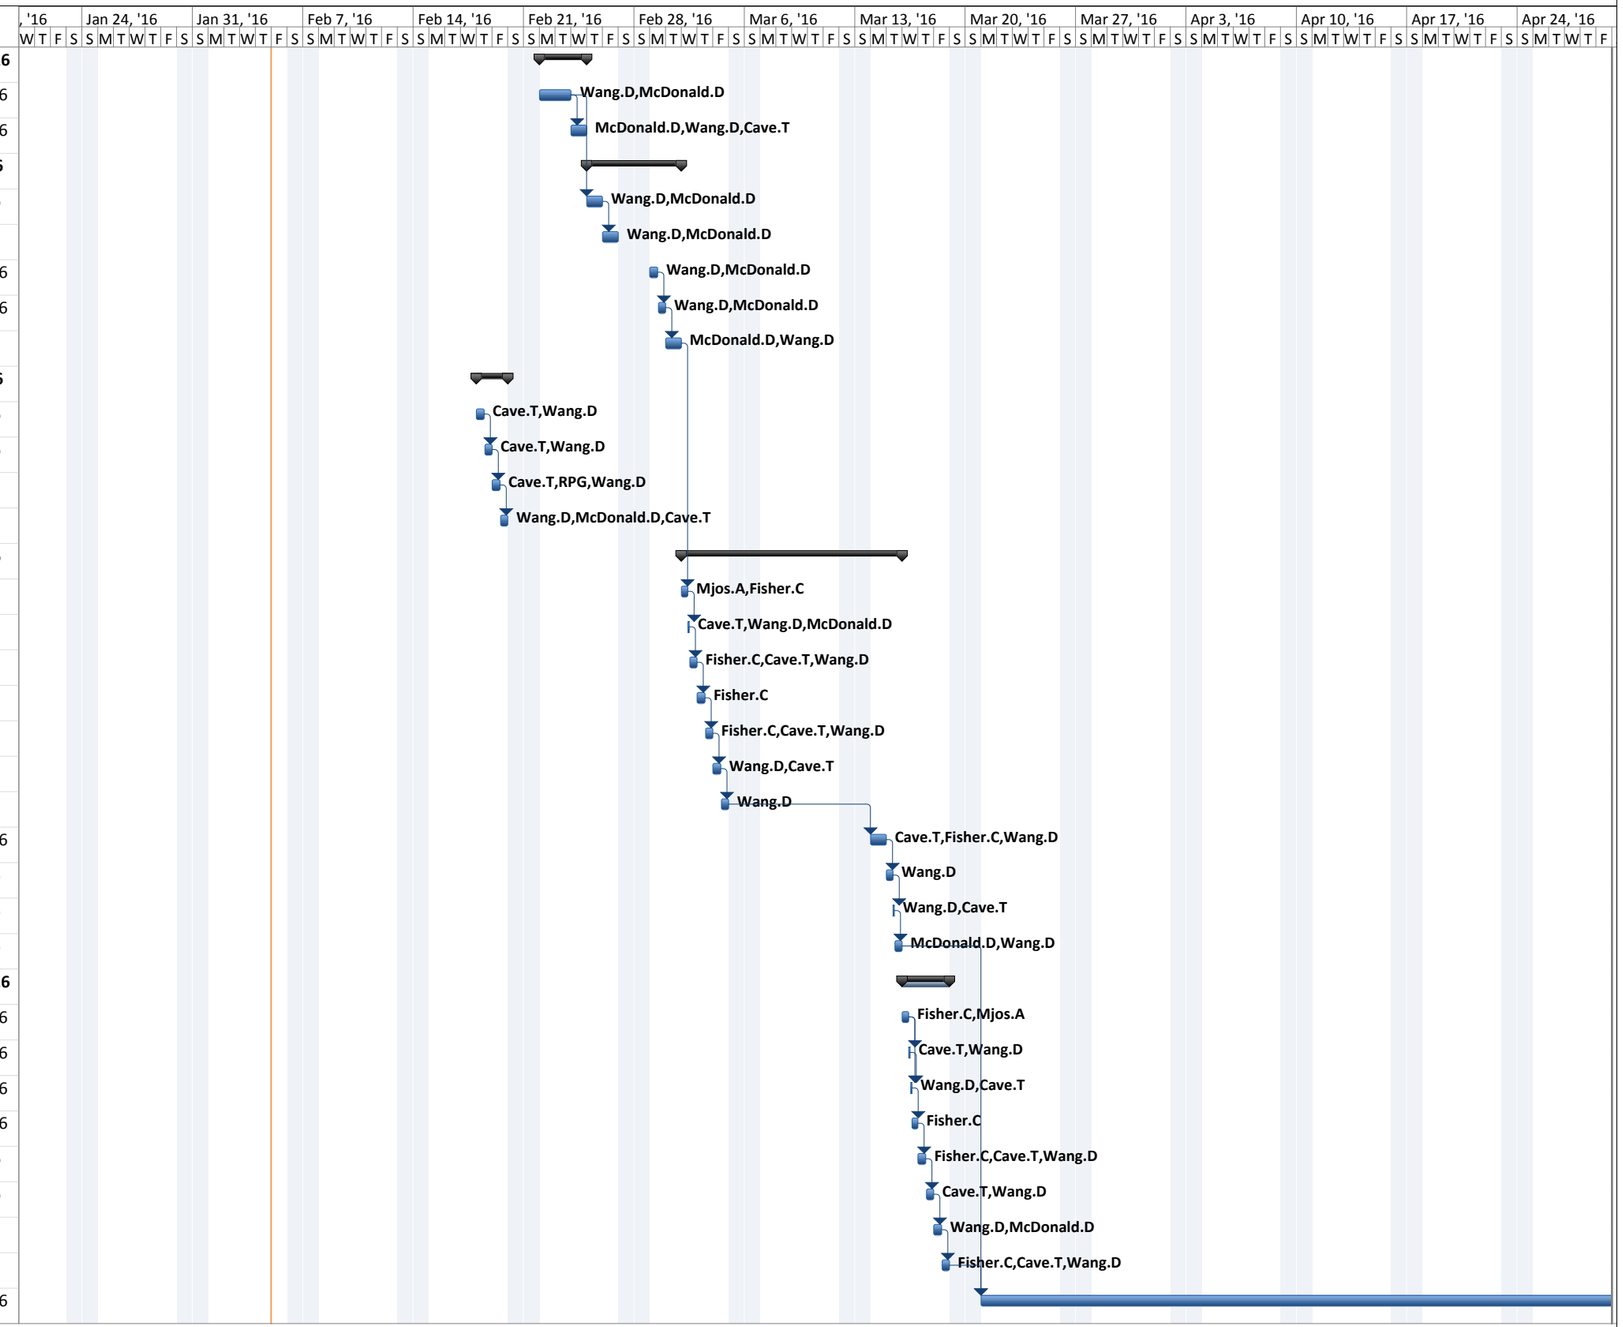

Project: 2016 winter shut down t
Date: Fri 2/5/16

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress	
