2016 WINTER SHUT DOWN TARGET HALL SCHEDULE

ID		Task Mode	Task Name	Duration	Start	Finish	Pred	Resource Names
1	✓		**TM3 Service Chase and Containment box Field Check**	**2 days**	**Mon 2/15/16**	**Tue 2/16/16**		
3	✓		**TARGET HALL WATER SYSTEM UPGRADE**	**5 days**	**Wed 2/17/16**	**Tue 2/23/16**		
6	✓		**Shut Down Leak Check - Target Stations and Modules**	**4 days**	**Wed 2/24/16**	**Mon 2/29/16**		
12	✓		**ISAC Spent targets Shipment**	**6 days**	**Thu 2/11/16**	**Thu 2/18/16**		
17	✓		ITH MP1 Replacement	1 day	Thu 3/10/16	Thu 3/10/16		Vacuum Group,Wa
18	✓		**TM1 with New Lp Ucx target to ITW**	**14.75 days**	**Wed 3/16/16**	**Tue 4/5/16**		
42	✓		**TM4 with New Lp Ta Target to ITE**	**5 days**	**Wed 4/6/16**	**Tue 4/12/16**		
43	✓		New Lp Ta Target Insert into SHC	0.1 days	Wed 4/6/16	Wed 4/6/16	41	Fisher.C,Mjos.A
44	✓		Module Move -TM4-ITE to SHC	0.3 days	Wed 4/6/16	Wed 4/6/16	43	Cave.T,Wang.D
45	✓		Target Removal and Electrical Check	0.2 days	Wed 4/6/16	Wed 4/6/16	44	Wang.D,Cave.T
46	✓		New Target Installation	0.2 days	Wed 4/6/16	Wed 4/6/16	45	Fisher.C
47	✓		Leak Check and Electrical Check	0.2 days	Wed 4/6/16	Wed 4/6/16	46	Fisher.C,Cave.T,Wa
48	✓		Module Move -TM4-SHC to TCS	0.5 days	Thu 4/7/16	Thu 4/7/16	47	Cave.T,Wang.D
49	✓		Module Connection- TM4 -TCS/ Start of Pumps	0.5 days	Thu 4/7/16	Thu 4/7/16	48	Wang.D,McDonald.
50	✓		Target Inspection	0.5 days	Fri 4/8/16	Fri 4/8/16	49	Fisher.C,Mjos.A
51	✓		Spent Target Move	0.5 days	Mon 4/11/16	Mon 4/11/16	50	Cave.T,Fisher.C,Wa
52	✓		Module Check-TM4 -TCS-Electrical, Vacuum	0.5 days	Mon 4/11/16	Mon 4/11/16	51	Cave.T,Wang.D
53	✓		Module Move- TM4-TCS to ITE	0.5 days	Tue 4/12/16	Tue 4/12/16	52	Cave.T,McDonald.D
54	✓		Module Connection-TM4 -ITE/ Start of Pumps	0.5 days	Tue 4/12/16	Tue 4/12/16	53	McDonald.D,Wang.
55			**TM2 Check in TCS**	**14 days**	**Wed 4/13/16**	**Mon 5/2/16**		
56	✓		Module Move-TM2-Silo to TCS	0.5 days	Wed 4/13/16	Wed 4/13/16		Cave.T,Wang.D
57	✓		Module Connection-TM2-TCS/ Start of Pumps	0.5 days	Wed 4/13/16	Wed 4/13/16	56	Wang.D
58	✓		Module Pump Down-TM2 -TCS	6 days	Thu 4/14/16	Thu 4/21/16	57	
59			Module Check-TM2 -TCS-Vacuum, Helium, Water	6 days	Fri 4/22/16	Fri 4/29/16	58	Mjos.A,Wang.D
60			Module disconnection-TM2-TCS	0.5 days	Mon 5/2/16	Mon 5/2/16	59	Wang.D
61			Module Move- TM2-TCS to Silo	0.5 days	Mon 5/2/16	Mon 5/2/16	60	Cave.T,Wang.D
62			TM3 Refurbishment	9 days	Wed 5/4/16	Mon 5/16/16	61	RPG,Target Group ,

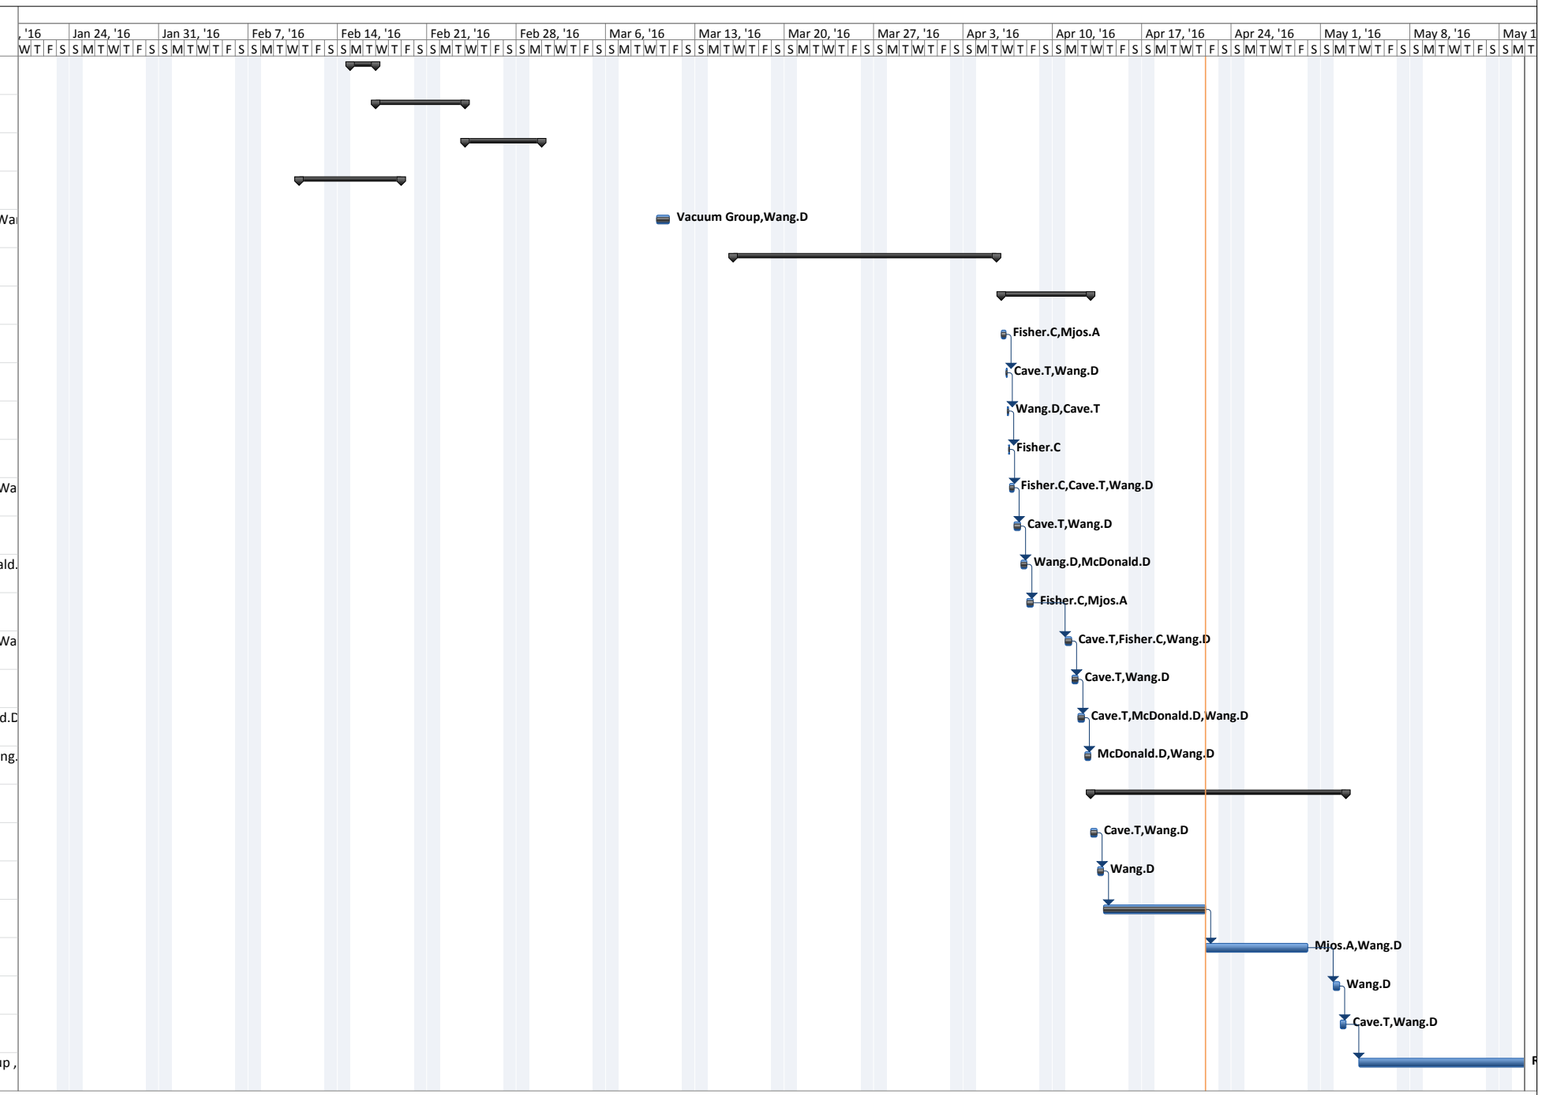

Project: 2016 winter shut down t
Date: Fri 4/22/16

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress	
