ID		Task Mode	Task Name	Duration	Start	Finish	Predec
1	✓		**TM2 HpTa Ready for ITW**	**11 days**	**Tue 8/23/16**	**Tue 9/6/16**	
11			**TM4 LpSiC IGLIS Target Ready for ITE**	**11 days**	**Tue 9/20/16**	**Tue 10/4/16**	
12	✓		Lp SiC Target Insert into SHC	0.1 days	Tue 9/20/16	Tue 9/20/16	10
13	✓		Module Disconnection TM4-ITE	0.25 days	Tue 9/20/16	Tue 9/20/16	12
14	✓		Module Move-TM4-ITE to SHC	0.25 days	Tue 9/20/16	Tue 9/20/16	13
15	✓		LpSiC Target Installation/Electrical check-SHC	0.25 days	Tue 9/20/16	Tue 9/20/16	14
16	✓		Module Move-TM4-SHC to CS/Start of Pumps	1 day	Wed 9/21/16	Wed 9/21/16	15
17	✓		Spent Target Move	1 day	Thu 9/22/16	Thu 9/22/16	16
18	✓		Module Move-TM4-TCS to ITE	0.5 days	Tue 9/27/16	Tue 9/27/16	17
19	✓		Module Connection-TM4-ITW/Start of Pumps	0.5 days	Tue 9/27/16	Tue 9/27/16	18
20			Shielding Blocks Transfer-ITW to ITE	1 day	Tue 10/4/16	Tue 10/4/16	19
21			**TM2 HpSiC FEBIAD Target Ready for ITW**	**11 days**	**Tue 10/11/16**	**Tue 10/25/16**	
22			HpSiC FEBIAD Target Insert into SHC	0.25 days	Tue 10/11/16	Tue 10/11/16	20
23			Module Disconnection-TM2-ITW	0.25 days	Tue 10/11/16	Tue 10/11/16	22
24			Module Move-TM2-ITW to SHC	0.25 days	Tue 10/11/16	Tue 10/11/16	23
25			New Target Installation/Electrical Check	0.5 days	Wed 10/12/16	Wed 10/12/16	24
26			Module Move-TM2-SHC to CS/Start of Pumps	0.5 days	Wed 10/12/16	Wed 10/12/16	25
27			Spent Target Move	1 day	Thu 10/13/16	Thu 10/13/16	26
28			Module Move-TM2-TCS to ITW	0.5 days	Tue 10/18/16	Tue 10/18/16	27
29			Module Connection-TM2-ITW/Start of Pumps	0.5 days	Tue 10/18/16	Tue 10/18/16	28
30			Shielding Blocks Transfer-ITE to ITW	1 day	Tue 10/25/16	Tue 10/25/16	29
31			**TM4 HpTa Target Ready for ITE**	**11 days**	**Tue 11/1/16**	**Tue 11/15/16**	
32			HpTa Target Insert into SHC	0.25 days	Tue 11/1/16	Tue 11/1/16	30
33			Module Disconnection-TM4-ITE	0.25 days	Tue 11/1/16	Tue 11/1/16	32
34			Module Move-TM4-ITE to SHC	0.25 days	Tue 11/1/16	Tue 11/1/16	33
35			New Target Installation/Electrical Check	0.5 days	Wed 11/2/16	Wed 11/2/16	34
36			Module Move-TM4-SHC to CS/Start of Pumps	0.5 days	Wed 11/2/16	Wed 11/2/16	35
37			Spent Target Move	1 day	Thu 11/3/16	Thu 11/3/16	36
38			Module Move-TM4-TCS to ITE	0.5 days	Tue 11/8/16	Tue 11/8/16	37
39			Module Connection-TM4-ITE/Start of Pumps	0.5 days	Tue 11/8/16	Tue 11/8/16	38
40			Shielding Blocks Transfer-ITW to ITE	1 day	Tue 11/15/16	Tue 11/15/16	39
41			**TM2 Ucx Target Ready for ITW**	**11 days**	**Tue 11/22/16**	**Tue 12/6/16**	
42			UCX Target Insert into SHC	0.1 days	Tue 11/22/16	Tue 11/22/16	40
43			Module Disconnection-TM2-ITW	0.2 days	Tue 11/22/16	Tue 11/22/16	42
44			Module Move-TM2-ITW to SHC	0.2 days	Tue 11/22/16	Tue 11/22/16	43
45			New Target Installation/Electrical Check	0.2 days	Tue 11/22/16	Tue 11/22/16	44
46			Module Move-TM2-SHC to CS/Start of Pumps	0.1 days	Tue 11/22/16	Tue 11/22/16	45
47			Spent Target Move	1 day	Wed 11/23/16	Wed 11/23/16	46
48			Module Move-TM2-TCS to ITW	0.5 days	Tue 11/29/16	Tue 11/29/16	47
49			Module Connection-TM2-ITW/Start of Pumps	0.5 days	Tue 11/29/16	Tue 11/29/16	48
50			Shielding Blocks Transfer-ITE to ITW	1 day	Tue 12/6/16	Tue 12/6/16	

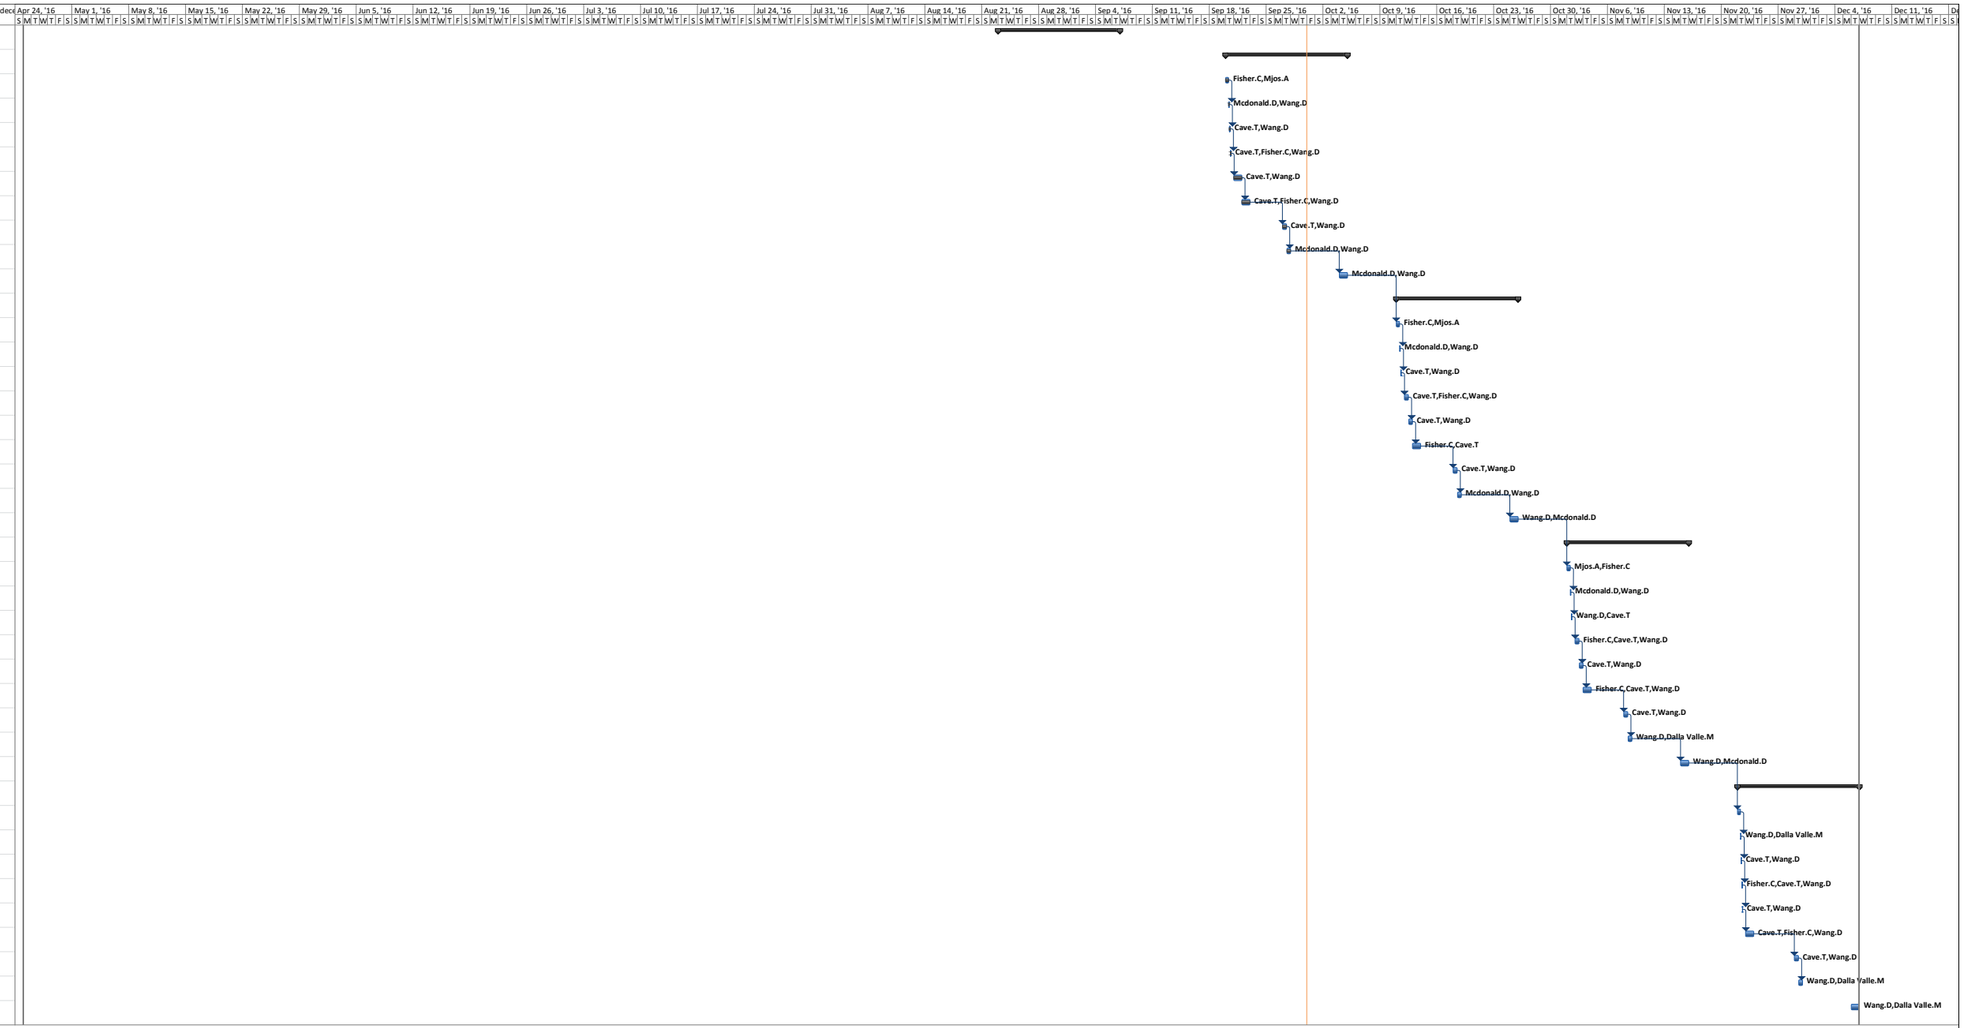

Project: Target Hall shedule 131 S
Date: Fri 9/30/16

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
