ID	Task Mode	Task Name	Duration	Start	Finish	Predecs
1		**TM2 LpTa Ready for ITW**	**30 days**	**Mon 4/25/16**	**Fri 6/3/16**	
24		**TM4 LP Ucx Ready for ITE**	**15 days**	**Tue 6/7/16**	**Mon 6/27/16**	
36		**TM2 HpSiC Ready for ITW**	**10 days**	**Tue 7/5/16**	**Mon 7/18/16**	
48		**TM4 LP Ucx Ready for ITE**	**10 days**	**Tue 8/2/16**	**Mon 8/15/16**	
60		**TM2 HpTa Ready for ITE**	**11 days**	**Tue 8/23/16**	**Tue 9/6/16**	
61		HpTa Target Insert into SHC	0.25 days	Tue 8/23/16	Tue 8/23/16	59
62		Module Disconnection-TM2-ITW	0.25 days	Tue 8/23/16	Tue 8/23/16	61
63		Module Move-TM2-ITW to SHC	0.25 days	Tue 8/23/16	Tue 8/23/16	62
64		New Target Installation/Electrical Check	0.5 days	Wed 8/24/16	Wed 8/24/16	63
65		Module Move-TM2-SHC to CS/Start of Pumps	0.5 days	Wed 8/24/16	Wed 8/24/16	64
66		Spent Target Move	1 day	Thu 8/25/16	Thu 8/25/16	65
67		Module Move-TM2-TCS to ITW	0.5 days	Tue 8/30/16	Tue 8/30/16	66
68		Module Connection-TM2-ITW/Start of Pumps	0.5 days	Tue 8/30/16	Tue 8/30/16	67
69		Shielding Blocks Transfer-ITE to ITW	1 day	Tue 9/6/16	Tue 9/6/16	68
70		**TM4 LpSiC Target Ready for ITE**	**11 days?**	**Tue 9/20/16**	**Tue 10/4/16**	
71		Lp SiC Target Insert into SHC	0.1 days	Tue 9/20/16	Tue 9/20/16	69
72		Module Disconnection TM4-ITE	0.25 days	Tue 9/20/16	Tue 9/20/16	71
73		Module Move-TM4-ITE to SHC	0.25 days?	Tue 9/20/16	Tue 9/20/16	72
74		LpSiC Target Installation/Electrical check-SHC	0.25 days	Tue 9/20/16	Tue 9/20/16	73
75		Module Move-TM4-SHC to CS/Start of Pumps	1 day	Wed 9/21/16	Wed 9/21/16	74
76		Spent Target Move	1 day	Thu 9/22/16	Thu 9/22/16	75
77		Module Move-TM4-TCS to ITE	0.5 days	Tue 9/27/16	Tue 9/27/16	76
78		Module Connection-TM4-ITW/Start of Pumps	0.5 days	Tue 9/27/16	Tue 9/27/16	77
79		Shielding Blocks Transfer-ITW to ITE	1 day	Tue 10/4/16	Tue 10/4/16	

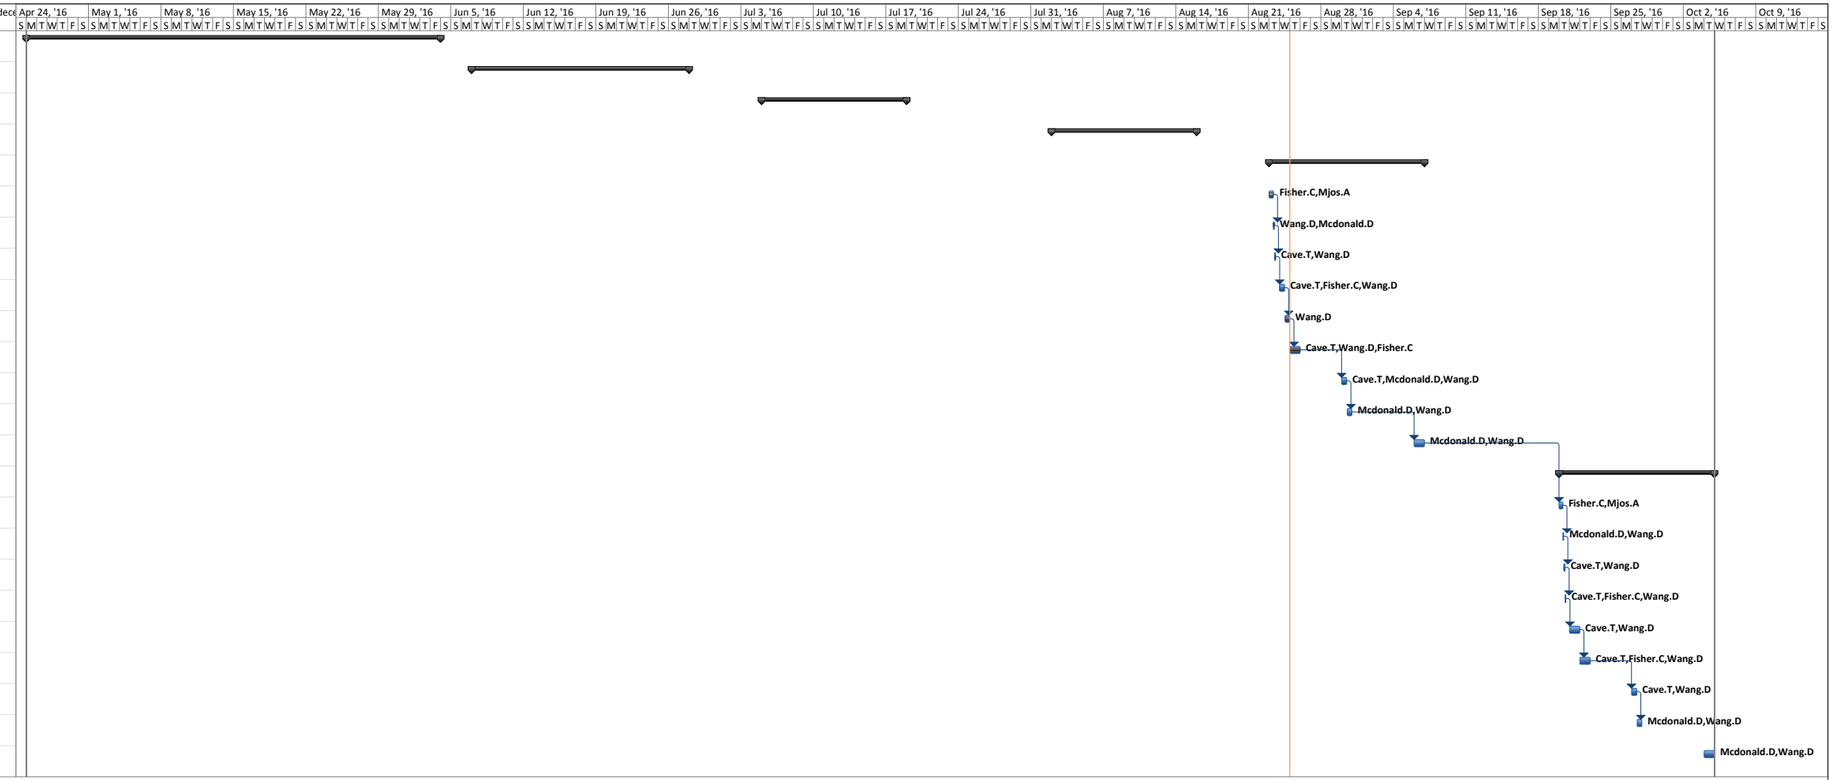

Project: Target Hall shedule 130 A
Date: Thu 8/25/16

Task		Milestone		Project Summary		External Milestone		Inactive Milestone		Manual Task		Manual Summary Rollup		Start-only		Deadline	
Split		Summary		External Tasks		Inactive Task		Inactive Summary		Duration-only		Manual Summary		Finish-only		Progress	
